

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1		UPDATED as of April 1 2024																			
2		SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21																
3		SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18																
4		SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18																
5		SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18																
6		SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19																
7		SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19																
8		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 5/21/19	Tue 5/21/19																
9		SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20																
10		SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20																
11		SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20																
12		SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20																
13		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 5/7/20	Thu 5/7/20																
14		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20																
15		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20																
16		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20																
17		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20																
18		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20																
19		SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20																
20		SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21																
21		SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21																
22		SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19																
23		SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19																
24		SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19																
25		SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19																
26		SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19																
27		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 9/24/19	Tue 9/24/19																
28		SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20																
29		SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20																
30		SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20																
31		SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20																
32		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 5/7/20	Thu 5/7/20																
33		SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20																
34		SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20																
35		SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20																
36		SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20																
37		SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20																
38		SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20																

Project: IOU Master Task Timeli

Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks





































External Milestone


Deadline

Progress

Manual Progress

Page 1

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025																				
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2																					
115		SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21																																			
116		SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21																																			
117		SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21																																			
118		SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22																																			
119		SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22																																			
120		SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21																																			
121		SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21																																			
122		SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21																																			
123		SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21																																			
124		SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21																																			
125		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 4/29/21	Thu 4/29/21																																			
126		SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21																																			
127		SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21																																			
128		SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21																																			
129		SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21																																			
130		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Mon 8/30/21	Mon 8/30/21																																			
131		SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21																																			
132		SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22																																			
133		SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22																																			
134		SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22																																			
135		SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22																																			
136		SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22																																			
137		SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22																																			
138		SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23																																			
139		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22																																			
140		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22																																			
141		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22																																			
142		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22																																			
143		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22																																			
144		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 6/7/22	Tue 6/7/22																																			
145		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22																																			
146		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22																																			
147		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22																																			
148		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22																																			
149		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22																																			
150		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22																																			
151		SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23																																			
152		SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23																																			

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
153		SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23																
154		SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22																
155		SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23																
156		SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23																
157																					
158		SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23																
159		SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22																
160		SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22																
161		SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22																
162		SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22																
163		SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22																
164		SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 6/7/22	Tue 6/7/22																
165		SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22																
166		SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22																
167		SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22																
168		SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22																
169		SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22																
170		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22																
171		SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23																
172		SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23																
173		SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23																
174		SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22																
175		SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23																
176		SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23																
177		SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24																
178		SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23																
179		SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23																
180		SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23																
181		SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23																
182		SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23																
183		SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23																
184		SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23																
185		SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24																
186		SCE - Submit Advice Letter	20 days	Wed 1/31/24	Tue 2/27/24																
187		SCE - Advice Letter Approved	23 days	Fri 3/1/24	Tue 4/2/24																
188		SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25																
189		SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23																
190		SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div>	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
191		SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23																
192		SCE - RFP Paused	59 days	Fri 10/13/23	Wed 1/3/24																
193		SCE - RFP Re-Issue Preparation	40 days	Wed 1/3/24	Tue 2/27/24																
194		SCE - RFP Re-Issue Release	1 day	Wed 2/28/24	Wed 2/28/24																
195		SCE - RFP Proposal Creation Duration	44 days	Wed 2/28/24	Mon 4/29/24																
196		SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24																
197		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Mon 7/29/24	Mon 7/29/24																
198		SCE - Contract Negotiation and Development	89 days	Tue 7/30/24	Fri 11/29/24																
199		SCE - Contract Review with EE PRG	1 day	Tue 6/18/24	Tue 6/18/24																
200		SCE - Final Award and Contract Signed	1 day?	Wed 3/5/25	Wed 3/5/25																
201		SCE - Submit Advice Letter	20 days?	Thu 3/6/25	Wed 4/2/25																
202		SCE - Advice Letter Approved	1 day	Wed 5/7/25	Wed 5/7/25																
203		SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24																
204		SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23																
205		SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23																
206		SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24																
207		SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24																
208		SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24																
209		SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Wed 2/28/24	Wed 2/28/24																
210		SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24																
211		SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24																
212		SCE - Final Award and Contract Signed	12 days	Mon 7/29/24	Tue 8/13/24																
213		SCE - Submit Advice Letter	34 days	Wed 8/14/24	Mon 9/30/24																
214		SCE - Advice Letter Approved	1 day	Fri 11/29/24	Fri 11/29/24																
215		SCE - Local Large Industrial	293 days?	Fri 11/3/23	Tue 12/17/24																
216		SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23																
217		SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23																
218		SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24																
219		SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24																
220		SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24																
221		SCE - RFP Estimated Notification of Successful and Unsuccessful Bi	1 day	Tue 4/23/24	Tue 4/23/24																
222		SCE - Contract Negotiation and Development	73 days	Wed 4/24/24	Fri 8/2/24																
223		SCE - Contract Review with EE PRG	1 day	Tue 9/17/24	Tue 9/17/24																
224		SCE - Final Award and Contract Signed	10 days	Wed 10/2/24	Tue 10/15/24																
225		SCE - Submit Advice Letter	23 days	Wed 10/16/24	Fri 11/15/24																
226		SCE - Advice Letter Approved	22 days	Mon 11/18/24	Tue 12/17/24																
227		SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25																
228		SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div>	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
343		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20																
344		SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20																
345		SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21																
346		SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21																
347		SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21																
348		SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19																
349		SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19																
350		SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19																
351		SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19																
352		SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19																
353		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	0 days	Fri 1/24/20	Fri 1/24/20																
354		SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19																
355		SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20																
356		SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20																
357		SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20																
358		SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20																
359		SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	0 days	Fri 5/15/20	Fri 5/15/20																
360		SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20																
361		SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20																
362		SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20																
363		SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20																
364		SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21																
365		SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21																
366		SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21																
367		SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20																
368		SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20																
369		SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20																
370		SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20																
371		SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20																
372		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Fri 5/15/20	Fri 5/15/20																
373		SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20																
374		SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20																
375		SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20																
376		SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20																
377		SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20																
378		SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 12/7/20	Mon 12/7/20																
379		SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21																
380		SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


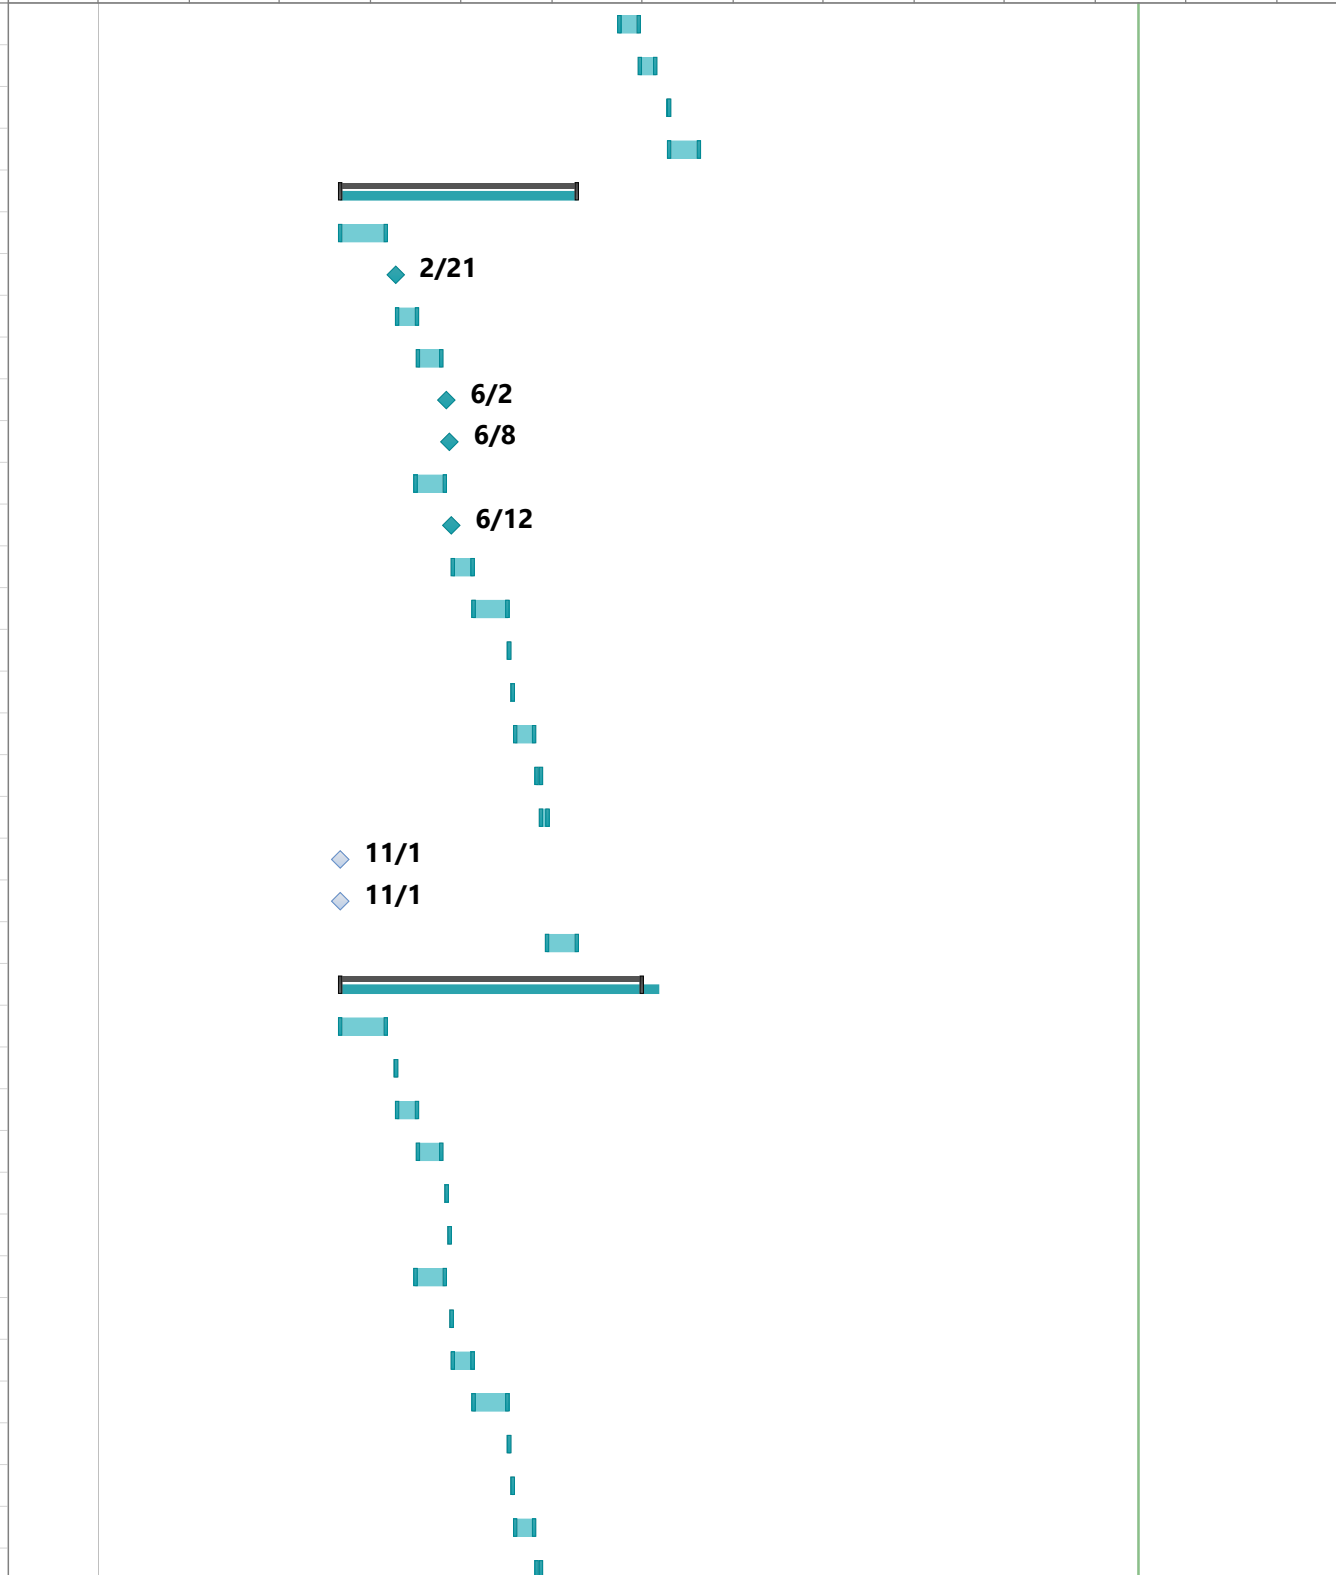
External Tasks




















External Milestone

Deadline


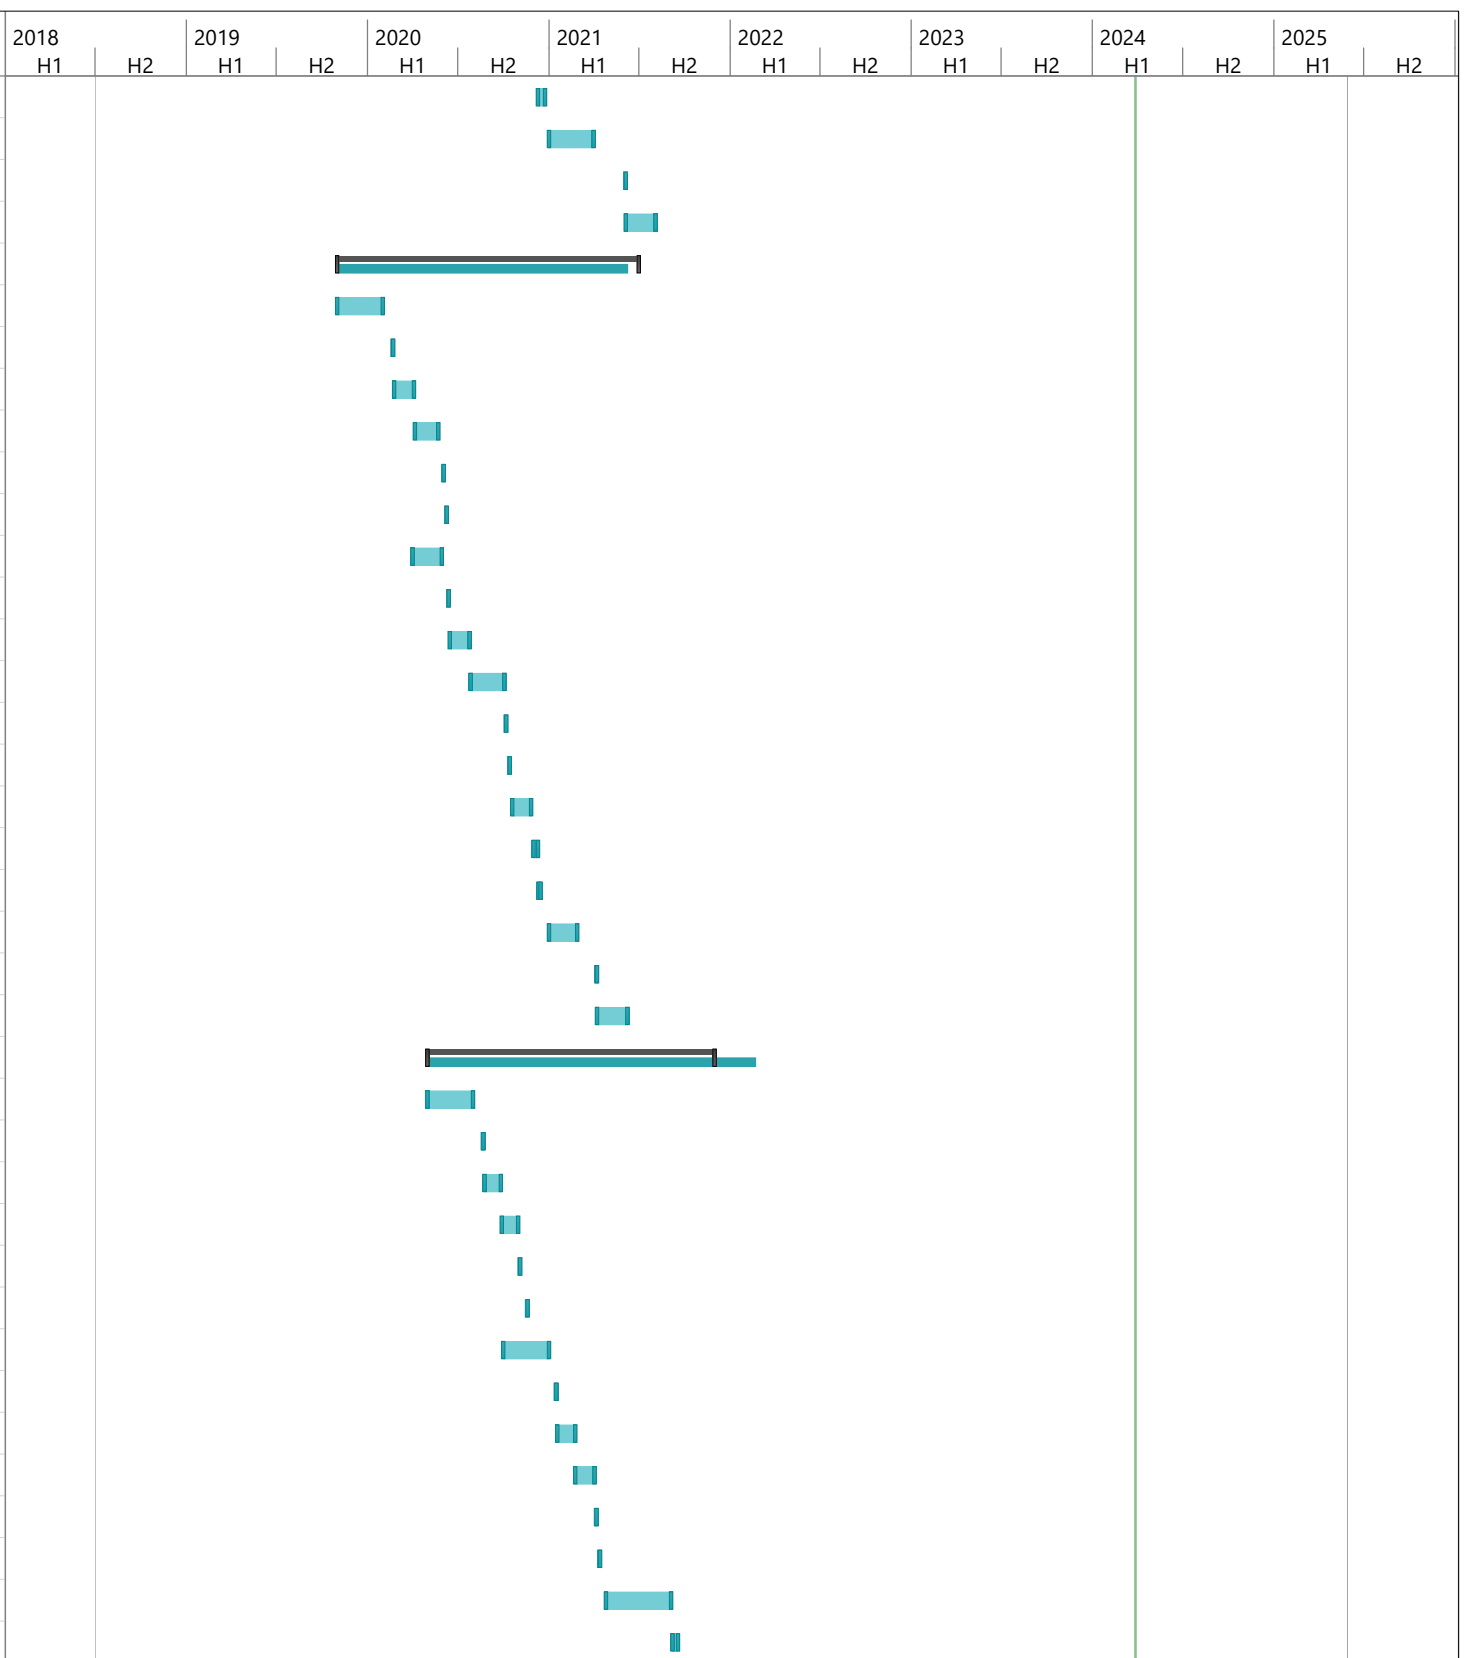
Progress


Manual Progress


ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2		
381		SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21																
382		SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21																
383		SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21																
384		SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21																
385		SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21																
386		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20																
387		SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20																
388		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20																
389		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20																
390		SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20																
391		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	0 days	Mon 6/8/20	Mon 6/8/20																
392		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20																
393		SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20																
394		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20																
395		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20																
396		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20																
397		SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 10/13/20	Tue 10/13/20																
398		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20																
399		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20																
400		SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20																
401		SCG - Submit Advice Letter	0 days	N/A	N/A																
402		SCG - Advice Letter Approved	0 days	N/A	N/A																
403		SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21																
404		SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21																
405		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20																
406		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20																
407		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20																
408		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20																
409		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20																
410		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 6/8/20	Mon 6/8/20																
411		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20																
412		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20																
413		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20																
414		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20																
415		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20																
416		SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 10/13/20	Tue 10/13/20																
417		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20																
418		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20																

Project: IOU Master Task Timeli Date: Thu 3/28/24	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

Page 11

ID		Task Name	Duration	Start	Finish																								
						2018			2019			2020			2021			2022			2023			2024			2025		
						H1	H2		H1	H2		H1	H2		H1	H2		H1	H2		H1	H2		H1	H2		H1	H2	
419		SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20																								
420		SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21																								
421		SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21																								
422		SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21																								
423		SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21																								
424		SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20																								
425		SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20																								
426		SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20																								
427		SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20																								
428		SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20																								
429		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 6/8/20	Mon 6/8/20																								
430		SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20																								
431		SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20																								
432		SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20																								
433		SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20																								
434		SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20																								
435		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 10/13/20	Tue 10/13/20																								
436		SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20																								
437		SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20																								
438		SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20																								
439		SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21																								
440		SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21																								
441		SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21																								
442		SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21																								
443		SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20																								
444		SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20																								
445		SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20																								
446		SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20																								
447		SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20																								
448		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidc	1 day	Wed 11/18/20	Wed 11/18/20																								
449		SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20																								
450		SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21																								
451		SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21																								
452		SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21																								
453		SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21																								
454		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 4/13/21	Tue 4/13/21																								
455		SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21																								
456		SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21																								

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
495		SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22																
496		SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22																
497		SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23																
498		SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23																
499		SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22																
500		SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21																
501		SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21																
502		SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21																
503		SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21																
504		SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21																
505		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 9/14/21	Tue 9/14/21																
506		SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21																
507		SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21																
508		SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21																
509		SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22																
510		SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22																
511		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 3/8/22	Tue 3/8/22																
512		SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22																
513		SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22																
514		SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22																
515		SCG - Submit Advice Letter	23 days	N/A	N/A																
516		SCG - Advice Letter Approved	1 day	N/A	N/A																
517		SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22																
518		SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22																
519		SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21																
520		SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21																
521		SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21																
522		SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21																
523		SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21																
524		SCG - RFA Estimated Notification of Successful and Unsuccessful Bidc	1 day	Tue 8/10/21	Tue 8/10/21																
525		SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21																
526		SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21																
527		SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21																
528		SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21																
529		SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21																
530		SCG - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 12/14/21	Tue 12/14/21																
531		SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22																
532		SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22																

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2		
533		SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22																
534		SCG - Submit Advice Letter	21 days	N/A	N/A																
535		SCG - Advice Letter Approved	1 day	N/A	N/A																
536		SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22																
537		SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
538		SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21																
539		SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21																
540		SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21																
541		SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21																
542		SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21																
543		SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 11/9/21	Tue 11/9/21																
544		SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21																
545		SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22																
546		SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22																
547		SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22																
548		SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22																
549		SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Wed 5/11/22	Wed 5/11/22																
550		SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22																
551		SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22																
552		SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22																
553		SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23																
554		SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23																
555		SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23																
556		SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22																
557		RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22																
558		RFA Release	1 day	Fri 3/25/22	Fri 3/25/22																
559		RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22																
560		RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22																
561		RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22																
562		RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22																
563		RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22																
564		RFP Release	1 day	Fri 6/24/22	Fri 6/24/22																
565		RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22																
566		RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22																
567		RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22																
568		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22																
569		Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22																
570		Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22																
<div><div><div>Project: IOU Master Task Timeline</div><div>Date: Thu 3/28/24</div></div><div><div><div>Task</div><div>Split</div><div>Milestone</div><div>Summary</div></div><div><div><div></div><div></div><div></div><div></div></div><div><div>Project Summary</div><div>Inactive Task</div><div>Inactive Milestone</div><div>Inactive Summary</div></div></div><div><div><div></div><div></div><div></div><div></div></div><div><div>Manual Task</div><div>Duration-only</div><div>Manual Summary Rollup</div><div>Manual Summary</div></div></div><div><div><div></div><div></div><div></div><div></div></div><div><div>Manual Task</div><div>Finish-only</div><div>External Tasks</div><div>External Milestone</div></div></div><div><div><div></div><div></div><div></div><div></div></div><div><div>Start-only</div><div>Manual Progress</div></div></div><div><div><div></div><div></div><div></div><div></div></div><div><div>Deadline</div><div>Progress</div><div>Manual Progress</div></div></div><div><div><div></div><div></div><div></div><div></div></div><div><div></div><div></div><div></div><div></div></div></div></div></div>																					
Page 15																					

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
571		Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22																
572		Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23																
573		Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23																
574		Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23																
575		SCG –Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23																
576		SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
577		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22																
578		RFP Release	1 day	Fri 5/13/22	Fri 5/13/22																
579		RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22																
580		RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22																
581		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22																
582		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22																
583		Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22																
584		Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22																
585		Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22																
586		Submit Advice Letter	N/A	N/A	N/A																
587		Advice Letter Approved	N/A	N/A	N/A																
588		Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23																
589		SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22																
590		RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22																
591		RFP Release	1 day	Fri 6/17/22	Fri 6/17/22																
592		RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22																
593		RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22																
594		RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22																
595		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22																
596		Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22																
597		Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22																
598		Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22																
599		Submit Advice Letter	N/A	N/A	N/A																
600		Advice Letter Approved	N/A	N/A	N/A																
601		Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22																
602		SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
603		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22																
604		RFP Release	1 day	Fri 8/26/22	Fri 8/26/22																
605		RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22																
606		RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22																
607		RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22																
608		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 16

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
609		Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22																
610		Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22																
611		Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22																
612		Submit Advice Letter	N/A	N/A	N/A																
613		Advice Letter Approved	N/A	N/A	N/A																
614		Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23																
615		SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
616		RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22																
617		RFP Release	1 day	Mon 7/25/22	Mon 7/25/22																
618		RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22																
619		RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22																
620		RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22																
621		RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22																
622		Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22																
623		Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22																
624		Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22																
625		Submit Advice Letter	N/A	N/A	N/A																
626		Advice Letter Approved	N/A	N/A	N/A																
627		Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22																
628		SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23																
629		RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23																
630		RFP Release	20 days	Thu 4/20/23	Wed 5/17/23																
631		RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23																
632		RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23																
633		RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23																
634		RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23																
635		Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23																
636		Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23																
637		Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23																
638		Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23																
639		Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23																
640		Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23																
641		SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24																
642		RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23																
643		RFP Release	13 days	Wed 9/13/23	Fri 9/29/23																
644		RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23																
645		RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23																
646		RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


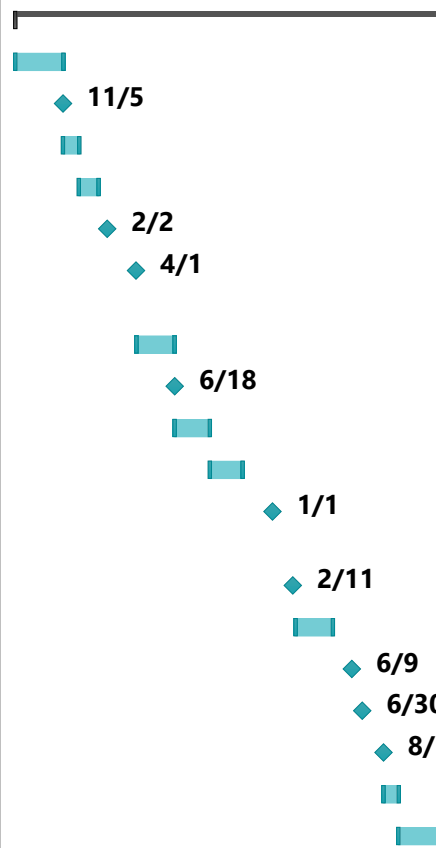











































External Tasks

External Milestone





































Deadline

Progress

Manual Progress

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
647		RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23																
648		Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23																
649		Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23																
650		Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23																
651		Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23																
652		Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23																
653		Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24																
654		<New Task>																			
655																					
656		<i>Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change</i>																			
657		SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20																
658		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18																
659		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18	 11/5															
660		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18																
661		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19																
662		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19	 2/2															
663		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19	 4/1															
664		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19																
665		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19	 6/18															
666		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19																
667		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19																
668		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20	 1/1															
669		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20	 2/11															
670		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20																
671		SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20	 6/9															
672		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20	 6/30															
673		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20	 8/12															
674		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20																
675		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20																
676		SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20																
677		SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18																
678		SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18	 11/5															
679		SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18																
680		SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19																
681		SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19	 2/2															
Project: IOU Master Task Timeli Date: Thu 3/28/24		Task		Project Summary		Manual Task		Start-only		Deadline											
		Split		Inactive Task		Duration-only		Finish-only		Progress											
		Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress											
		Summary		Inactive Summary		Manual Summary		External Milestone													

Page 18

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
682		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19			 4/1													
683		SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19																
684		SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19			 6/18													
685		SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19																
686		SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19																
687		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20					 1/1											
688		SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20					 2/11											
689		SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20																
690		SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20					 5/12											
691		SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20					 6/30											
692		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20					 8/12											
693		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20																
694		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20																
695		SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20																
696		SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18																
697		SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19																
698		SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18																
699		SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19																
700		SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18			 11/13													
701		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19			 3/20													
702		SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19																
703		SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19																
704		SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19																
705		SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19																
706		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19																
707		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20					 3/10											
708		SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20																
709		SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20																
710		SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20					 6/22											
711		SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20					 8/12											
712		SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20																
713		SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20																
714		SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21																
715		SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19																
716		SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19			 1/7													


Project: IOU Master Task Timeli
Date: Thu 3/28/24


Task


Split


Milestone

Summary











Project Summary


Inactive Task


Inactive Milestone

Inactive Summary











Manual Task


Duration-only


Manual Summary Rollup

Manual Summary











Start-only


Finish-only


External Tasks

External Milestone












Deadline





































Progress

Manual Progress









ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
717		SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19																
718		SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19																
719		SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19				4/9												
720		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19				4/17												
721		SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19																
722		SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19					9/3											
723		SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19																
724		SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19																
725		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20					1/21											
726		SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20					3/10											
727		SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20																
728		SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20					9/8											
729		SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20					10/30											
730		SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20					11/12											
731		SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20					12/11											
732		SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21					2/9											
733		SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22																
734		SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19																
735		SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19				5/10												
736		SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19																
737		SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19																
738		SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19				9/10												
739		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19				9/20												
740		SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19																
741		SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20					1/27											
742		SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20																
743		SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20																
744		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20					8/17											
745		SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21																
746		SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21																
747		SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21					11/9											
748		SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22					1/7											
749		SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22					1/10											
750		SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22					2/10											
751		SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22																

Project: IOU Master Task Timeli
Date: Thu 3/28/24


Task




Project Summary




Manual Task




Start-only




Deadline




Split




Inactive Task




Duration-only




Finish-only




Progress




Milestone




Inactive Milestone




Manual Summary Rollup




External Tasks




Manual Progress




Summary




Inactive Summary




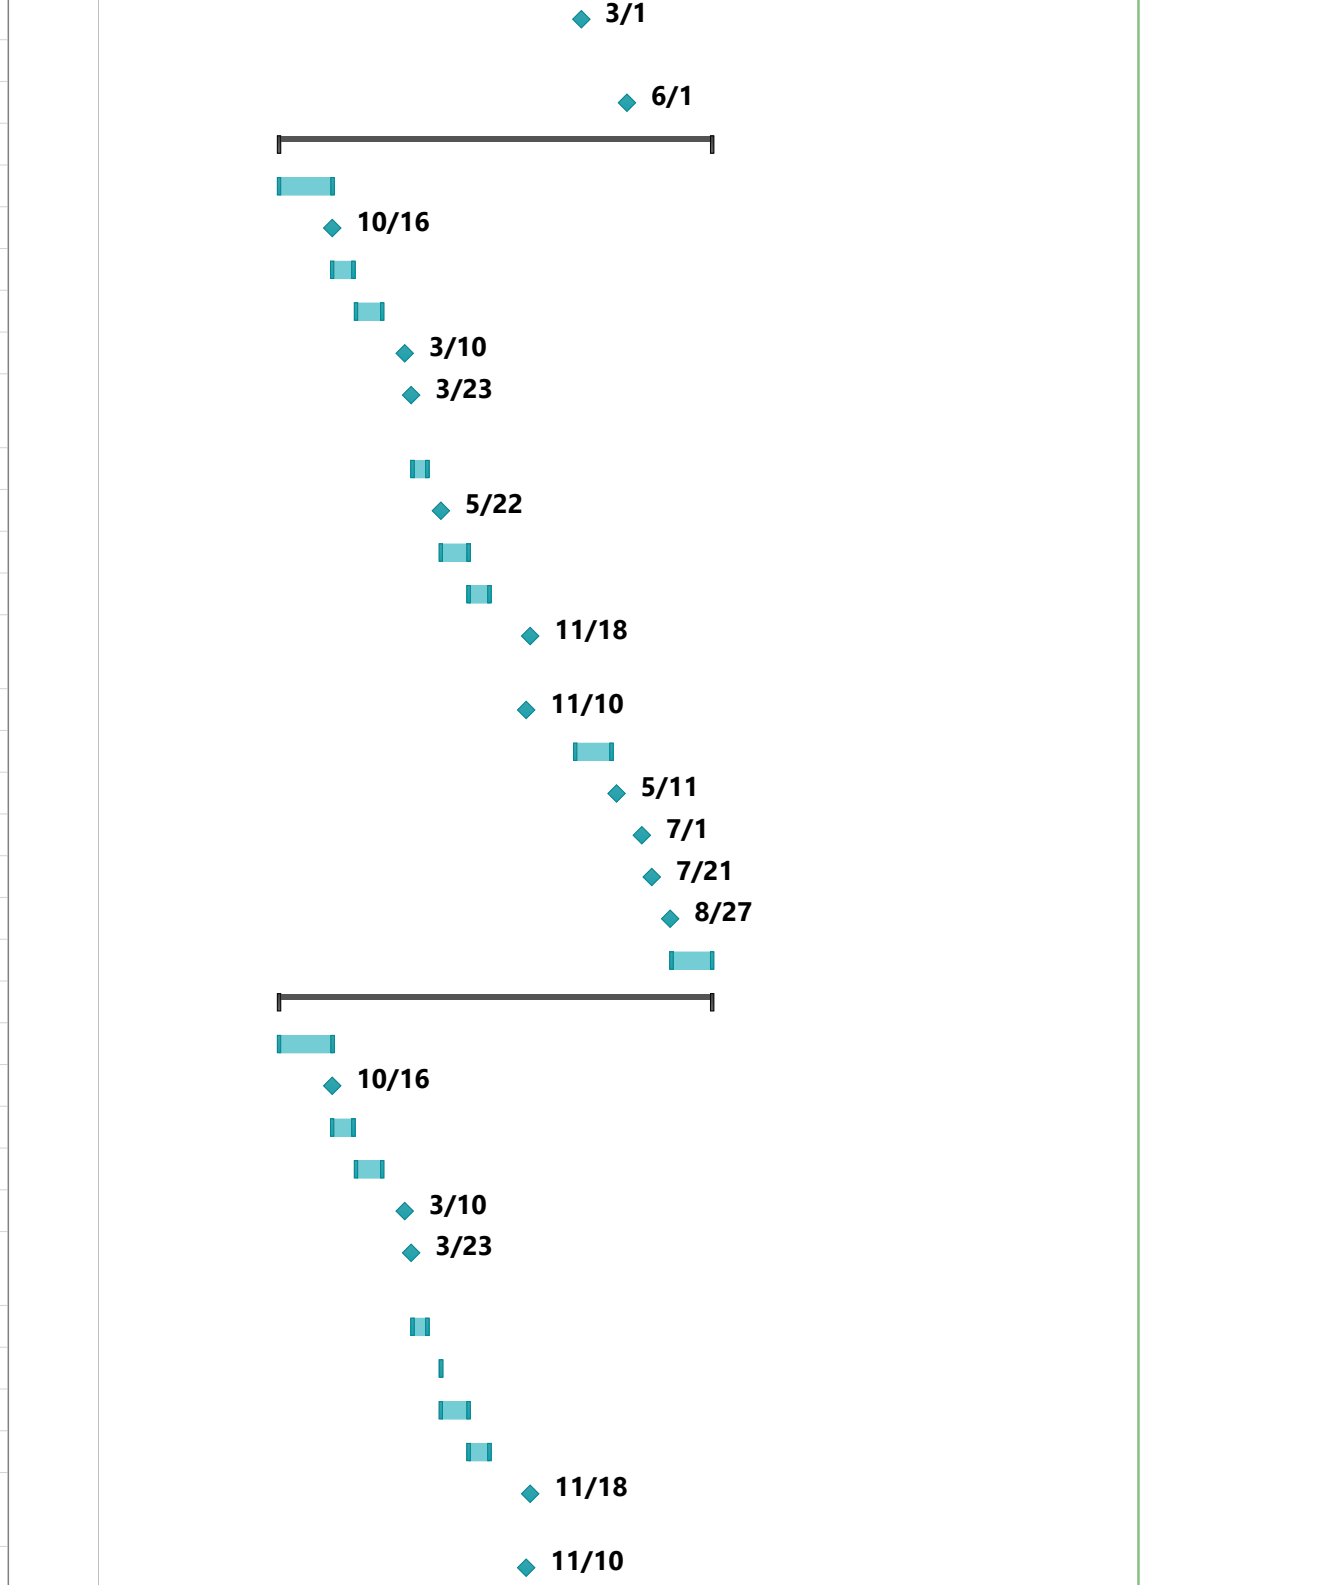
Manual Summary



External Milestone



Page 20

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
787		SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21																
788		SDG&E - Advice Letter Approved																			
789		SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21																
790		SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21																
791		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19																
792		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19																
793		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19																
794		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20																
795		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20																
796		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20																
797		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20																
798		SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20																
799		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20																
800		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20																
801		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20																
802		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20																
803		SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21																
804		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21																
805		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21																
806		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21																
807		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21																
808		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21																
809		SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21																
810		SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19																
811		SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19																
812		SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19																
813		SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20																
814		SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20																
815		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20																
816		SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20																
817		SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20																
818		SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20																
819		SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20																
820		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20																
821		SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20																

Project: IOU Master Task Timeli

Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone




















Deadline

Progress


Manual Progress

Page 22

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
822		SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21																
823		SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21																
824		SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21																
825		SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21																
826		SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21																
827		SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21																
828		SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22																
829		SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20																
830		SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21																
831		SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21																
832		SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21																
833		SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21																
834		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21																
835		SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21																
836		SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21																
837		SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21																
838		SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21																
839		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21																
840		SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21																
841		SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21																
842		SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22																
843		SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22																
844		SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22																
845		SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22																
846		SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22																
847		SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22																
848		SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21																
849		SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21																
850		SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21																
851		SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21																
852		SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21																
853		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21																
854		SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21																
855		SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21																
856		SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21																
857		SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21																

Project: IOU Master Task Timeli Date: Thu 3/28/24	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

Page 23

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025		
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	
858		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22																	
859		SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22																	
860		SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22																	
861		SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22																	
862		SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21																	
863		SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22																	
864		SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22																	
865		SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22																	
866		*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22																	
867		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21																	
868		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21																	
869		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21																	
870		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21																	
871		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21																	
872		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21																	
873		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21																	
874		SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21																	
875		SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22																	
876		SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22																	
877		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22																	
878		SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22																	
879		SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22																	
880		SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22																	
881		SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22																	
882		SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22																	
883		SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22																	
884		SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23																	
885		*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22																	
886		SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21																	
887		SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21																	
888		SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21																	
889		SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21																	
890		SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21																	
891		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21																	
892		SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21																	

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 24

ID	<div><div></div><div></div><div>i</div></div>	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
929		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21																
930		SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21																
931		SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21																
932		SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22																
933		SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22																
934		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22																
935		SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22																
936		SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22																
937		SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22																
938		SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22																
939		SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22																
940		SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22																
941		SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23																
942		*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23																
943		SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22																
944		SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22																
945		SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22																
946		SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22																
947		SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22																
948		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22																
949		SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22																
950		SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22																
951		SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22																
952		SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23																
953		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23																
954		SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23																
955		SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23																
956		SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23																
957		SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23																
958		SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23																
959		SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23																
960		SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23																
961		*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitation	353 days?	Mon 1/16/23	Wed 5/22/24																
962		SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div>	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
963		SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23																
964		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23																
965		SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23																
966		SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23																
967		SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23																
968		SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23																
969		SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24																
970		SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24																
971		SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24																
972		*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24																
973		SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23																
974		SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23																
975		SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23																
976		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23																
977		SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23																
978		SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23																
979		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23																
980		SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23																
981		SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23																
982		SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24																
983		SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24																
984		SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24																
985		SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24																
986		SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24																
987		*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24																
988		SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22																
989		SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22																
990		SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22																
991		SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22																
992		SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23																
993		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23																
994		SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22																
995		SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23																
996		SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23																
997		SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23																

Project: IOU Master Task Timeli

Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone





















Deadline


Progress

Manual Progress

Page 27

[illegible]

ID		Task Name	Duration	Start	Finish	2018	H1	H2	2019	H1	H2	2020	H1	H2	2021	H1	H2	2022	H1	H2	2023	H1	H2	2024	H1	H2	2025	H1	H2
1069		SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24																								
1070		SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24																								
1071		SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24																								
1072		SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24																								
1073		SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24																								
1074		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24																								
1075		SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24																								
1076		SDG&E - Contract Negotiation and Development	60 days	Wed 7/17/24	Tue 10/8/24																								
1077		SDG&E - Contract Review with EE PRG	9 days	Thu 11/7/24	Tue 11/19/24																								
1078		SDG&E - Final Award and Contract Signed	1 day	Tue 11/19/24	Tue 11/19/24																								
1079		SDG&E - Submit Advice Letter	1 day	Mon 1/6/25	Mon 1/6/25																								
1080		SDG&E - Advice Letter Approved	1 day	Thu 2/6/25	Thu 2/6/25																								
1081		SDG&E - Implementation Plan	46 days	Fri 3/21/25	Fri 5/23/25																								
1082		*SDG&E - Market Access Program (MAP)	317 days	Wed 3/13/24	Thu 5/29/25																								
1083		SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24																								
1084		SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24																								
1085		SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24																								
1086		SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24																								
1087		SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24																								
1088		SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24																								
1089		SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24																								
1090		SDG&E - Contract Review with EE PRG	7 days	Thu 1/9/25	Fri 1/17/25																								
1091		SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25																								
1092		SDG&E - Submit Advice Letter	1 day	Fri 2/14/25	Fri 2/14/25																								
1093		SDG&E - Advice Letter Approved	1 day	Mon 3/31/25	Mon 3/31/25																								
1094		SDG&E - Implementation Plan	44 days	Mon 3/31/25	Thu 5/29/25																								
1095		Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change																											
1096																													
1097		PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20																								
1098		PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19																								
1099		PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19																								
1100		PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19																								
1101		PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19																								
1102		PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19																								
Project: IOU Master Task Timeli Date: Thu 3/28/24		Task		Project Summary		Manual Task		Start-only		Deadline																			
		Split		Inactive Task		Duration-only		Finish-only		Progress																			
		Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress																			
		Summary		Inactive Summary		Manual Summary		External Milestone																					
Page 30																													

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1103		PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19																
1104		PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19																
1105		PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19																
1106		PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19																
1107		PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20																
1108		PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20																
1109		PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20																
1110		PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20																
1111		PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20																
1112		PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20																
1113		PG&E - Submit Advice Letter		N/A	N/A																
1114		PG&E - Advice Letter Approved																			
1115		PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20																
1116		PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20																
1117		PG&E - RFA Preparation		N/A	N/A																
1118		PG&E - RFA Release		N/A	N/A																
1119		PG&E - RFA Abstract Creation Duration		N/A	N/A																
1120		PG&E - RFA Evaluation		N/A	N/A																
1121		PG&E - RFA Review with EE PRG		N/A	N/A																
1122		PG&E - RFA Estimated Notification of Successful and Unsuccessful		N/A	N/A																
1123		PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19																
1124		PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19																
1125		PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19																
1126		PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19																
1127		PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19																
1128		PG&E - RFP Estimated Notification of Successful and Unsuccessful	3 days	Wed 11/27/19	Fri 11/29/19																
1129		PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20																
1130		PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20																
1131		PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20																
1132		PG&E - Submit Advice Letter		N/A	N/A																
1133		PG&E - Advice Letter Approved																			
1134		PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20																
1135		PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21																
1136		PG&E - RFA Preparation		N/A	N/A																
1137		PG&E - RFA Release		N/A	N/A																
1138		PG&E - RFA Abstract Creation Duration		N/A	N/A																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div>	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1139		PG&E - RFA Evaluation		N/A	N/A																
1140		PG&E - RFA Review with EE PRG		N/A	N/A																
1141		PG&E - RFA Estimated Notification of Successful and Unsuccessful		N/A	N/A																
1142		PG&E - RFP Preparation		N/A	N/A																
1143		PG&E - RFP Release		N/A	N/A																
1144		PG&E - RFP Proposal Creation Duration		N/A	N/A																
1145		PG&E - RFP Evaluation		N/A	N/A																
1146		PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20																
1147		PG&E - RFP Estimated Notification of Successful and Unsuccessful																			
1148		PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20																
1149		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20																
1150		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20																
1151		PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21																
1152		PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21																
1153		PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21																
1154		PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21																
1155		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19																
1156		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19																
1157		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19																
1158		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19																
1159		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19																
1160		PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Tue 8/27/19	Fri 8/30/19																
1161		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20																
1162		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20																
1163		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20																
1164		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20																
1165		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20																
1166		PG&E - RFP Estimated Notification of Successful and Unsuccessful	6 days	Wed 8/5/20	Wed 8/12/20																
1167		PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20																
1168		PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20																
1169		PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20																
1170		PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21																
1171		PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21																
1172		PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21																
1173		PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21																
1174		PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19																
1175		PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19																
1176		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div>	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1177		PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19																
1178		PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19																
1179		PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Tue 8/27/19	Fri 8/30/19																
1180		PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20																
1181		PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20																
1182		PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20																
1183		PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20																
1184		PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20																
1185		PG&E - RFP Estimated Notification of Successful and Unsuccessful	6 days	Wed 8/5/20	Wed 8/12/20																
1186		PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21																
1187		PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21																
1188		PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21																
1189		PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21																
1190		PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21																
1191		PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21																
1192		PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21																
1193		PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21																
1194		PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21																
1195		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20																
1196		PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20																
1197		PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20																
1198		PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20																
1199		PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20																
1200		PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Fri 7/3/20	Wed 7/8/20																
1201		PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20																
1202		PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20																
1203		PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20																
1204		PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20																
1205		PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20																
1206		PG&E - RFP Estimated Notification of Successful and Unsuccessful	1 day	Tue 11/10/20	Tue 11/10/20																
1207		PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21																
1208		PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21																
1209		PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21																
1210		PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21																
1211		PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21																
1212		PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21																
1213		PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21																
1214		PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20																

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div> Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1253		PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21															
1254		PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21															
1255		PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21															
1256		PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21															
1257		PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22															
1258		PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22															
1259		PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22															
1260		PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22															
1261		PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22															
1262		PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22															
1263		PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22															
1264		PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22															
1265		PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22															
1266		PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22															
1267		PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23															
1268		PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22															
1269		PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22															
1270		PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22															
1271		PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22															
1272		PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22															
1273		PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22															
1274		PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22															
1275		PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22															
1276		PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22															
1277		PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22															
1278		PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23															
1279		PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23															
1280		PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23															
1281		PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23															
1282		PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23															
1283		PG&E - Submit Advice Letter		N/A																
1284		PG&E - Advice Letter Approved		N/A																
1285		PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23															
1286		PG&E - Residential Electrification Equity Program Solicitation	620 days	Mon 8/1/22	Fri 12/13/24															
1287		PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22															
1288		PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22															
1289		PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23															
1290		PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23															

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div> Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1291		PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23															
1292		PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23															
1293		PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23															
1294		PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23															
1295		PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23															
1296		PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23															
1297		PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23															
1298		PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23															
1299		PG&E - Contract Negotiation and Development	206 days	Tue 8/1/23	Tue 5/14/24															
1300		PG&E - Contract Review with EE PRG	1 day	Thu 5/30/24	Thu 5/30/24															
1301		PG&E - Final Award and Contract Signed	46 days	Fri 6/21/24	Fri 8/23/24															
1302		PG&E - Submit Advice Letter	1 day	Mon 9/2/24	Mon 9/2/24															
1303		PG&E - Advice Letter Approved	1 day	Mon 10/14/24	Mon 10/14/24															
1304		PG&E - Implementation Plan	1 day	Fri 12/13/24	Fri 12/13/24															
1305		PG&E - Statewide C&S Advocacy Solicitation	663 days	Tue 2/1/22	Thu 8/15/24															
1306		PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22															
1307		PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22															
1308		PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22															
1309		PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22															
1310		PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22															
1311		PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22															
1312		PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22															
1313		PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22															
1314		PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22															
1315		PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22															
1316		PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22															
1317		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22															
1318		PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23															
1319		PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23															
1320		PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23															
1321		PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23															
1322		PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23															
1323		PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23															
1324		PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23															
1325		PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24															
1326		PG&E - Submit Advice Letter	1 day	Mon 4/15/24	Mon 4/15/24															
1327		PG&E - Advice Letter Approved	1 day	Sat 6/15/24	Sat 6/15/24															
1328		PG&E - Implementation Plan	1 day	Thu 8/15/24	Thu 8/15/24															

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID	<div><div></div><div>i</div></div> Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1329		PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24															
1330		PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23															
1331		PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23															
1332		PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23															
1333		PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23															
1334		PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23															
1335		PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23															
1336		PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24															
1337		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24															
1338		PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24															
1339		PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24															
1340		PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24															
1341		PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24															
1342		PG&E - Residential Whole Home Load Management RFP	379 days	Tue 8/15/23	Fri 1/24/25															
1343		PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23															
1344		PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23															
1345		PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23															
1346		PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23															
1347		PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24															
1348		PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24															
1349		PG&E - Contract Negotiation and Development	91 days	Wed 3/13/24	Wed 7/17/24															
1350		PG&E - Contract Review with EE PRG	1 day	Tue 7/23/24	Tue 7/23/24															
1351		PG&E - Final Award and Contract Signed	42 days	Thu 8/8/24	Fri 10/4/24															
1352		PG&E - Submit Advice Letter	1 day	Tue 10/15/24	Tue 10/15/24															
1353		PG&E - Advice Letter Approved	1 day	Mon 11/25/24	Mon 11/25/24															
1354		PG&E - Implementation Plan	1 day	Fri 1/24/25	Fri 1/24/25															
1355		PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24															
1356		PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23															
1357		PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23															
1358		PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23															
1359		PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23															
1360		PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23															
1361		PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23															
1362		PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24															
1363		PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24															
1364		PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24															
1365		PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24															
1366		PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24															

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone

Deadline

Progress

Manual Progress

ID		Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025				
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2					
1405		PG&E - Advice Letter Approved	1 day	Wed 12/18/24	Wed 12/18/24																<div><div></div></div>			
1406		PG&E - Implementation Plan	1 day	Fri 2/14/25	Fri 2/14/25																			
1407																								
1408																								

Project: IOU Master Task Timeli
Date: Thu 3/28/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress
