


ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
1	UPDATED as of October 1, 2020														
2	SCE - Local RCI Solicitation	739 days?	Tue 8/21/18	Fri 6/18/21											
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18											
4	SCE - RFA Release	0 days	Fri 11/9/18	Fri 11/9/18											
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18											
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19											
7	SCE - RFA Review with EE PRG	0 days	Tue 4/16/19	Tue 4/16/19											
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/21/19	Tue 5/21/19											
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20											
10	SCE - RFP Release	0 days	Wed 1/22/20	Wed 1/22/20											
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20											
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20											
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 5/7/20	Thu 5/7/20											
14	SCE - RFP Review with EE PRG	0 days	Tue 4/21/20	Tue 4/21/20											
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20											
16	SCE - Contract Review with EE PRG	0 days	Tue 8/18/20	Tue 8/18/20											
17	SCE - Final Award and Contract Signed	0 days	Wed 9/30/20	Wed 9/30/20											
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20											
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20											
20	SCE - Implementation Plan	35 days	Mon 5/3/21	Fri 6/18/21											
21	SCE - SW Lighting	563 days	Wed 4/3/19	Fri 5/28/21											
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19											
23	SCE - RFA Release	0 days	Tue 7/2/19	Tue 7/2/19											
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19											
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19											
26	SCE - RFA Review with EE PRG	0 days	Tue 9/17/19	Tue 9/17/19											
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/24/19	Tue 9/24/19											
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20											
29	SCE - RFP Release	0 days	Thu 2/6/20	Thu 2/6/20											
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20											
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20											
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 5/7/20	Thu 5/7/20											
33	SCE - RFP Review with EE PRG	0 days	Tue 4/21/20	Tue 4/21/20											
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20											
35	SCE - Contract Review with EE PRG	0 days	Tue 8/18/20	Tue 8/18/20											
36	SCE - Final Award and Contract Signed	0 days	Wed 9/30/20	Wed 9/30/20											
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20											
38	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20											

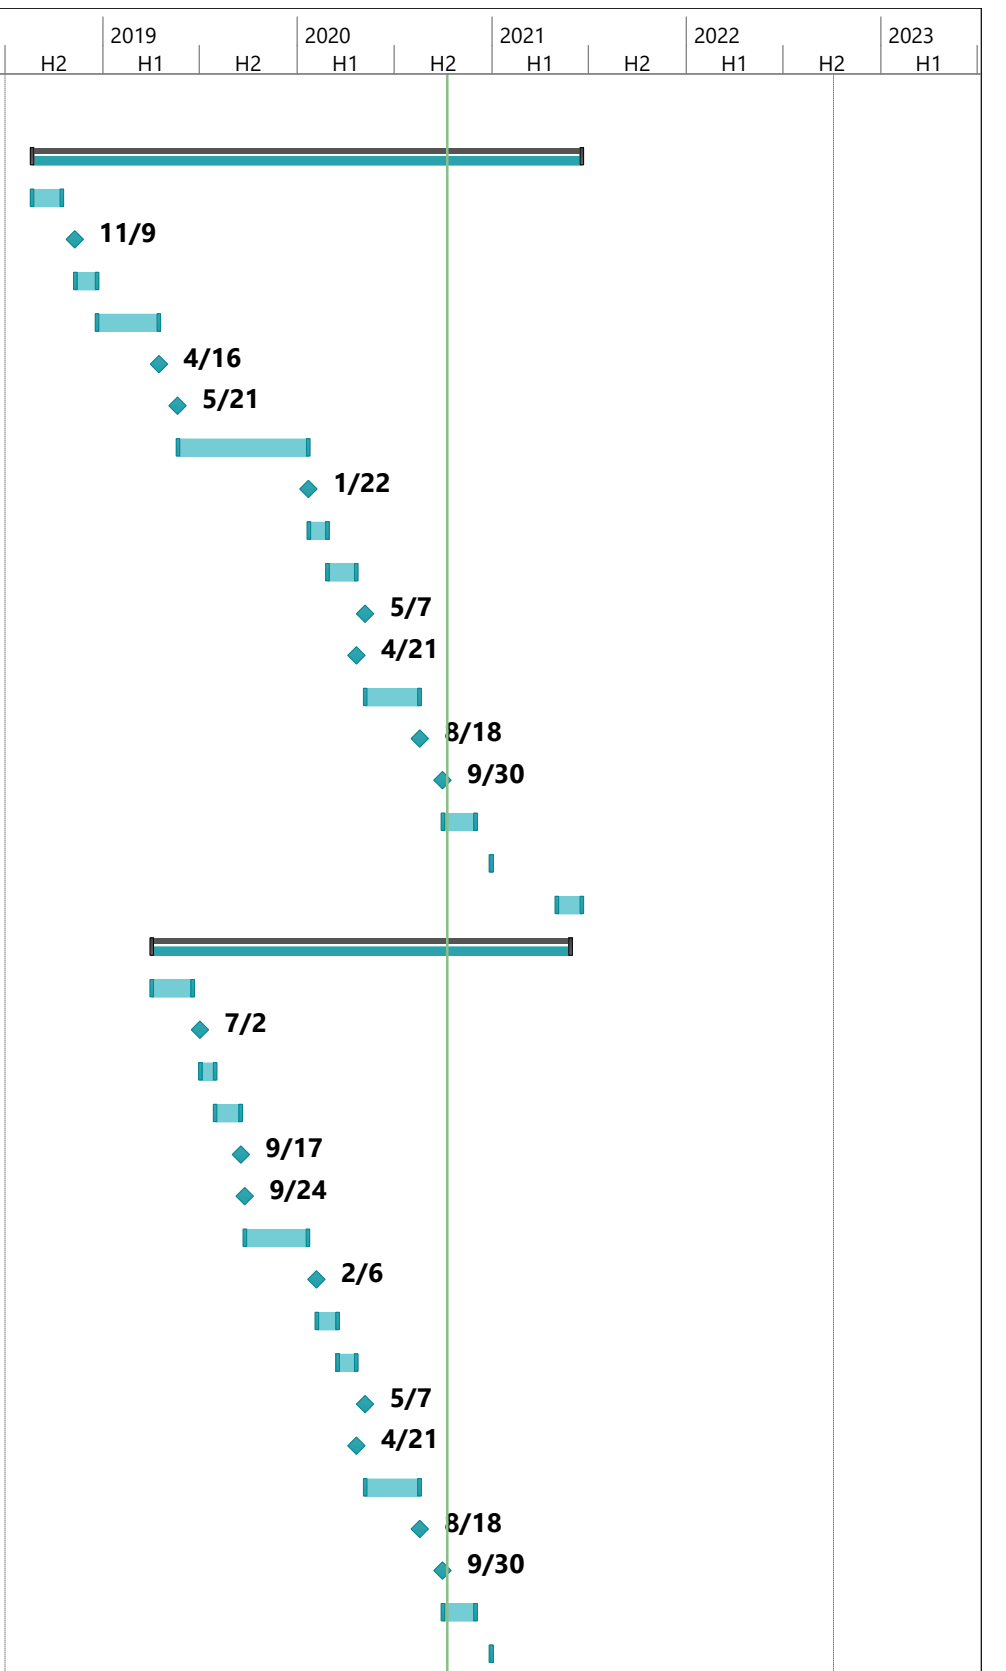

Project: IOU Master Task Timeli Date: Fri 10/9/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1		
39	SCE - Implementation Plan	42 days	Thu 4/1/21	Fri 5/28/21											
40	SCE - Local PAG Solicitation	385 days	Mon 8/31/20	Fri 2/18/22											
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20											
42	SCE - RFA Release	0 days	Thu 11/5/20	Thu 11/5/20											
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20											
44	SCE - RFA Evaluation	32 days	Fri 12/11/20	Mon 1/25/21											
45	SCE - RFA Review with EE PRG	0 days	Tue 1/19/21	Tue 1/19/21											
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21											
47	SCE - RFP Preparation	23 days	Thu 12/10/20	Mon 1/11/21											
48	SCE - RFP Release	0 days	Thu 4/1/21	Thu 4/1/21											
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21											
50	SCE - RFP Evaluation	14 days	Fri 5/14/21	Wed 6/2/21											
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/29/21	Tue 6/29/21											
52	SCE - RFP Review with EE PRG	0 days	Tue 6/15/21	Tue 6/15/21											
53	SCE - Contract Negotiation and Development	65 days	Tue 6/29/21	Mon 9/27/21											
54	SCE - Contract Review with EE PRG	0 days	Tue 10/19/21	Tue 10/19/21											
55	SCE - Final Award and Contract Signed	0 days	Fri 10/29/21	Fri 10/29/21											
56	SCE - Submit Advice Letter	0 days	Wed 12/1/21	Wed 12/1/21											
57	SCE - Advice Letter Approved	1 day	Tue 1/4/22	Tue 1/4/22											
58	SCE - Implementation Plan	45 days	Mon 12/20/21	Fri 2/18/22											
59	SCE - SW Water/Wastewater Solicitation	381 days	Mon 11/16/20	Mon 5/2/22											
60	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21											
61	SCE - RFA Release	0 days	Thu 3/4/21	Thu 3/4/21											
62	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21											
63	SCE - RFA Evaluation	18 days	Wed 4/14/21	Fri 5/7/21											
64	SCE - RFA Review with EE PRG	0 days	Tue 5/18/21	Tue 5/18/21											
65	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 5/27/21	Thu 5/27/21											
66	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21											
67	SCE - RFP Release	0 days	Thu 7/1/21	Thu 7/1/21											
68	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21											
69	SCE - RFP Evaluation	22 days	Fri 8/6/21	Mon 9/6/21											
70	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 9/27/21	Mon 9/27/21											
71	SCE - RFP Review with EE PRG	0 days	Tue 9/21/21	Tue 9/21/21											
72	SCE - Contract Negotiation and Development	29 days	Wed 9/22/21	Mon 11/1/21											
73	SCE - Contract Review with EE PRG	0 days	Tue 11/16/21	Tue 11/16/21											
74	SCE - Final Award and Contract Signed	0 days	Mon 12/20/21	Mon 12/20/21											
75	SCE - Submit Advice Letter	24 days	Tue 1/4/22	Fri 2/4/22											
76	SCE - Advice Letter Approved	1 day	Fri 3/4/22	Fri 3/4/22											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
77	SCE - Implementation Plan	46 days	Mon 2/28/22	Mon 5/2/22											
78	SCE - SW ETP Solicitation	402 days	Fri 5/1/20	Mon 11/15/21											
79	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20											
80	SCE - RFA Release	0 days	Tue 8/4/20	Tue 8/4/20											
81	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20											
82	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20											
83	SCE - RFA Review with EE PRG	0 days	Tue 10/20/20	Tue 10/20/20											
84	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 10/27/20	Tue 10/27/20											
85	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20											
86	SCE - RFP Release	0 days	Tue 12/8/20	Tue 12/8/20											
87	SCE - RFP Proposal Creation Duration	34 days	Tue 12/8/20	Fri 1/22/21											
88	SCE - RFP Evaluation	28 days	Mon 1/25/21	Wed 3/3/21											
89	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 3/23/21	Tue 3/23/21											
90	SCE - RFP Review with EE PRG	0 days	Tue 3/16/21	Tue 3/16/21											
91	SCE - Contract Negotiation and Development	28 days	Wed 3/24/21	Fri 4/30/21											
92	SCE - Contract Review with EE PRG	0 days	Wed 5/19/21	Wed 5/19/21											
93	SCE - Final Award and Contract Signed	0 days	Tue 6/15/21	Tue 6/15/21											
94	SCE - Submit Advice Letter	0 days	Wed 6/16/21	Wed 6/16/21											
95	SCE - Advice Letter Approved	1 day	Fri 7/23/21	Fri 7/23/21											
96	SCE - Implementation Plan	43 days	Thu 9/16/21	Mon 11/15/21											
97	SCE - SW Higher-Education Solicitation	370 days	Mon 11/2/20	Fri 4/1/22											
98	SCE - RFA Preparation	68 days	Mon 11/2/20	Wed 2/3/21											
99	SCE - RFA Release	0 days	Thu 2/4/21	Thu 2/4/21											
100	SCE - RFA Abstract Creation Duration	21 days	Mon 2/8/21	Mon 3/8/21											
101	SCE - RFA Evaluation	16 days	Tue 3/9/21	Tue 3/30/21											
102	SCE - RFA Review with EE PRG	0 days	Tue 4/20/21	Tue 4/20/21											
103	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 4/29/21	Thu 4/29/21											
104	SCE - RFP Preparation	53 days	Mon 3/22/21	Wed 6/2/21											
105	SCE - RFP Release	0 days	Thu 6/3/21	Thu 6/3/21											
106	SCE - RFP Proposal Creation Duration	25 days	Fri 6/4/21	Thu 7/8/21											
107	SCE - RFP Evaluation	20 days	Fri 7/9/21	Thu 8/5/21											
108	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 9/2/21	Thu 9/2/21											
109	SCE - RFP Review with EE PRG	0 days	Tue 8/17/21	Tue 8/17/21											
110	SCE - Contract Negotiation and Development	31 days	Fri 9/3/21	Fri 10/15/21											
111	SCE - Contract Review with EE PRG	0 days	Tue 11/16/21	Tue 11/16/21											
112	SCE - Final Award and Contract Signed	0 days	Thu 12/2/21	Thu 12/2/21											
113	SCE - Submit Advice Letter	23 days	Fri 12/3/21	Tue 1/4/22											
114	SCE - Advice Letter Approved	1 day	Mon 2/7/22	Mon 2/7/22											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
115	SCE - Implementation Plan	46 days	Fri 1/28/22	Fri 4/1/22											
116															
117	SCG - Local Single Family Solicitation	699 days	Sun 7/1/18	Thu 3/4/21											
118	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18											
119	SCG - RFA Release	0 days	Mon 11/26/18	Mon 11/26/18											
120	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19											
121	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19											
122	SCG - RFA Review with EE PRG	0 days	Tue 3/5/19	Tue 3/5/19											
123	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/3/19	Mon 6/3/19											
124	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19											
125	SCG - RFP Release	0 days	Wed 7/31/19	Wed 7/31/19											
126	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19											
127	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19											
128	SCG - RFP Review with EE PRG	0 days	Tue 11/5/19	Tue 11/5/19											
129	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
130	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20											
131	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20											
132	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20											
133	SCG - Submit Advice Letter	88 days	Mon 6/1/20	Wed 9/30/20											
134	SCG - Advice Letter Approved	1 day	Thu 12/31/20	Thu 12/31/20											
135	SCG - Implementation Plan	44 days	Mon 1/4/21	Thu 3/4/21											
136	SCG - Local Multi-family Solicitation	720 days	Sun 7/1/18	Fri 4/2/21											
137	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18											
138	SCG - RFA Release	0 days	Mon 11/26/18	Mon 11/26/18											
139	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19											
140	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19											
141	SCG - RFA Review with EE PRG	0 days	Tue 4/2/19	Tue 4/2/19											
142	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/3/19	Mon 6/3/19											
143	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19											
144	SCG - RFP Release	0 days	Wed 7/31/19	Wed 7/31/19											
145	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19											
146	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19											
147	SCG - RFP Review with EE PRG	0 days	Tue 11/5/19	Tue 11/5/19											
148	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
149	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20											
150	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20											
151	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20											
152	SCG - Submit Advice Letter	22 days	Thu 10/1/20	Fri 10/30/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
153	SCG - Advice Letter Approved	1 day	Fri 1/29/21	Fri 1/29/21											
154	SCG - Implementation Plan	45 days	Mon 2/1/21	Fri 4/2/21											
155	SCG - Local Small/Medium Commercial Solicitation	653 days	Tue 9/4/18	Thu 3/4/21											
156	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19											
157	SCG - RFA Release	0 days	Thu 1/31/19	Thu 1/31/19											
158	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19											
159	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19											
160	SCG - RFA Review with EE PRG	0 days	Tue 6/4/19	Tue 6/4/19											
161	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 8/1/19	Thu 8/1/19											
162	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19											
163	SCG - RFP Release	0 days	Fri 8/23/19	Fri 8/23/19											
164	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19											
165	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19											
166	SCG - RFP Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19											
167	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
168	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20											
169	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20											
170	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20											
171	SCG - Submit Advice Letter	34 days	Tue 9/1/20	Fri 10/16/20											
172	SCG - Advice Letter Approved	1 day	Thu 12/31/20	Thu 12/31/20											
173	SCG - Implementation Plan	44 days	Mon 1/4/21	Thu 3/4/21											
174	SCG - Local Small/Medium Public Solicitation	653 days	Tue 9/4/18	Thu 3/4/21											
175	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19											
176	SCG - RFA Release	0 days	Thu 1/31/19	Thu 1/31/19											
177	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19											
178	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19											
179	SCG - RFA Review with EE PRG	0 days	Tue 6/4/19	Tue 6/4/19											
180	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 8/1/19	Thu 8/1/19											
181	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19											
182	SCG - RFP Release	0 days	Fri 8/23/19	Fri 8/23/19											
183	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19											
184	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19											
185	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19											
186	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
187	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20											
188	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20											
189	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20											
190	SCG - Submit Advice Letter	29 days	Tue 9/1/20	Fri 10/9/20											

Project: IOU Master Task Timeli Date: Fri 10/9/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
191	SCG - Advice Letter Approved	0 days	Thu 12/31/20	Thu 12/31/20											
192	SCG - Implementation Plan	44 days	Mon 1/4/21	Thu 3/4/21											
193	SCG - Statewide POS Food Service Solicitation	595 days	Mon 1/21/19	Fri 4/30/21											
194	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19											
195	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19											
196	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19											
197	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19											
198	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19											
199	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20											
200	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19											
201	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20											
202	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20											
203	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20											
204	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20											
205	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20											
206	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20											
207	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20											
208	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20											
209	SCG - Submit Advice Letter	21 days	Mon 11/2/20	Mon 11/30/20											
210	SCG - Advice Letter Approved	0 days	Fri 2/26/21	Fri 2/26/21											
211	SCG - Implementation Plan	45 days	Mon 3/1/21	Fri 4/30/21											
212	SCG - Statewide Midstream Water Heating Solicitation	595 days	Mon 1/21/19	Fri 4/30/21											
213	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19											
214	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19											
215	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19											
216	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19											
217	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19											
218	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20											
219	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19											
220	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20											
221	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20											
222	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20											
223	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20											
224	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20											
225	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20											
226	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20											
227	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20											
228	SCG - Submit Advice Letter	21 days	Mon 11/2/20	Mon 11/30/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
229	SCG - Advice Letter Approved	0 days	Fri 2/26/21	Fri 2/26/21											
230	SCG - Implementation Plan	45 days	Mon 3/1/21	Fri 4/30/21											
231	SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Sat 10/30/21											
232	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20											
233	SCG - RFA Release	0 days	Wed 2/12/20	Wed 2/12/20											
234	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20											
235	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20											
236	SCG - RFA Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20											
237	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20											
238	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20											
239	SCG - RFP Release	0 days	Fri 8/21/20	Fri 8/21/20											
240	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20											
241	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20											
242	SCG - RFP Review with EE PRG	0 days	Tue 12/1/20	Tue 12/1/20											
243	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/8/20	Tue 12/8/20											
244	SCG - Contract Negotiation and Development	75 days	Mon 12/21/20	Fri 4/2/21											
245	SCG - Contract Review with EE PRG	14 days	Tue 4/6/21	Fri 4/23/21											
246	SCG - Final Award and Contract Signed	5 days	Mon 4/26/21	Fri 4/30/21											
247	SCG - Submit Advice Letter	22 days	Sat 5/1/21	Sun 5/30/21											
248	SCG - Advice Letter Approved	0 days	Tue 8/31/21	Tue 8/31/21											
249	SCG - Implementation Plan	44 days	Wed 9/1/21	Sat 10/30/21											
250	SCG - Local Manufactured Housing Solicitation	434 days	Fri 11/1/19	Wed 6/30/21											
251	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20											
252	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20											
253	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20											
254	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20											
255	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20											
256	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20											
257	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20											
258	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20											
259	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20											
260	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20											
261	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20											
262	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20											
263	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20											
264	SCG - Contract Review with EE PRG	14 days	Tue 12/1/20	Fri 12/18/20											
265	SCG - Final Award and Contract Signed	9 days	Mon 12/21/20	Thu 12/31/20											
266	SCG - Submit Advice Letter	21 days	Fri 1/1/21	Fri 1/29/21											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
267	SCG - Advice Letter Approved	0 days	Fri 4/30/21	Fri 4/30/21											
268	SCG - Implementation Plan	43 days	Mon 5/3/21	Wed 6/30/21											
269	SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21											
270	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20											
271	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20											
272	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20											
273	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20											
274	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20											
275	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20											
276	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20											
277	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20											
278	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20											
279	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20											
280	SCG - RFP Review with EE PRG	0 days	Tue 10/6/20	Tue 10/6/20											
281	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 10/13/20	Tue 10/13/20											
282	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20											
283	SCG - Contract Review with EE PRG	14 days	Tue 12/1/20	Fri 12/18/20											
284	SCG - Final Award and Contract Signed	9 days	Mon 12/21/20	Thu 12/31/20											
285	SCG - Submit Advice Letter	21 days	Fri 1/1/21	Fri 1/29/21											
286	SCG - Advice Letter Approved	0 days	Fri 4/30/21	Fri 4/30/21											
287	SCG - Implementation Plan	43 days	Mon 5/3/21	Wed 6/30/21											
288	SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21											
289	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20											
290	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20											
291	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20											
292	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20											
293	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20											
294	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20											
295	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20											
296	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20											
297	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20											
298	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20											
299	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20											
300	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20											
301	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20											
302	SCG - Contract Review with EE PRG	14 days	Tue 12/1/20	Fri 12/18/20											
303	SCG - Final Award and Contract Signed	9 days	Mon 12/21/20	Thu 12/31/20											
304	SCG - Submit Advice Letter	21 days	Fri 1/1/21	Fri 1/29/21											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
305	SCG - Advice Letter Approved	0 days	Fri 4/30/21	Fri 4/30/21											
306	SCG - Implementation Plan	43 days	Mon 5/3/21	Wed 6/30/21											
307	SCG - Local Behavioral Solicitation	413 days	Fri 5/1/20	Tue 11/30/21											
308	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20											
309	SCG - RFA Release	0 days	Fri 8/21/20	Fri 8/21/20											
310	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20											
311	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20											
312	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20											
313	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 11/10/20	Tue 11/10/20											
314	SCG - RFP Preparation	40 days	Thu 10/1/20	Wed 11/25/20											
315	SCG - RFP Release	0 days	Fri 12/11/20	Fri 12/11/20											
316	SCG - RFP Proposal Creation Duration	30 days	Mon 12/14/20	Fri 1/22/21											
317	SCG - RFP Evaluation	25 days	Mon 1/25/21	Fri 2/26/21											
318	SCG - RFP Review with EE PRG	0 days	Tue 3/2/21	Tue 3/2/21											
319	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 3/9/21	Tue 3/9/21											
320	SCG - Contract Negotiation and Development	30 days	Mon 3/22/21	Fri 4/30/21											
321	SCG - Contract Review with EE PRG	14 days	Tue 5/4/21	Fri 5/21/21											
322	SCG - Final Award and Contract Signed	7 days	Mon 5/24/21	Tue 6/1/21											
323	SCG - Submit Advice Letter	22 days	Tue 6/1/21	Wed 6/30/21											
324	SCG - Advice Letter Approved	0 days	Thu 9/30/21	Thu 9/30/21											
325	SCG - Implementation Plan	43 days	Fri 10/1/21	Tue 11/30/21											
326	SCG - Outreach Solicitation	434 days	Sun 11/1/20	Thu 6/30/22											
327	SCG - RFA Preparation	65 days	Sun 11/1/20	Thu 1/28/21											
328	SCG - RFA Release	0 days	Fri 2/19/21	Fri 2/19/21											
329	SCG - RFA Abstract Creation Duration	25 days	Mon 2/22/21	Fri 3/26/21											
330	SCG - RFA Evaluation	25 days	Mon 3/29/21	Fri 4/30/21											
331	SCG - RFA Review with EE PRG	0 days	Tue 5/4/21	Tue 5/4/21											
332	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/11/21	Tue 5/11/21											
333	SCG - RFP Preparation	42 days	Thu 4/1/21	Fri 5/28/21											
334	SCG - RFP Release	0 days	Fri 6/11/21	Fri 6/11/21											
335	SCG - RFP Proposal Creation Duration	30 days	Mon 6/14/21	Fri 7/23/21											
336	SCG - RFP Evaluation	30 days	Mon 7/26/21	Fri 9/3/21											
337	SCG - RFP Review with EE PRG	0 days	Tue 9/7/21	Tue 9/7/21											
338	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/14/21	Tue 9/14/21											
339	SCG - Contract Negotiation and Development	35 days	Mon 10/18/21	Fri 12/3/21											
340	SCG - Contract Review with EE PRG	9 days	Tue 12/7/21	Fri 12/17/21											
341	SCG - Final Award and Contract Signed	10 days	Mon 12/20/21	Fri 12/31/21											
342	SCG - Submit Advice Letter	21 days	Mon 1/3/22	Mon 1/31/22											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1		
343	SCG - Advice Letter Approved	0 days	Fri 4/29/22	Fri 4/29/22											
344	SCG - Implementation Plan	44 days	Mon 5/2/22	Thu 6/30/22											
345	SCG - Marketplace Solicitation	435 days?	Sun 11/1/20	Thu 6/30/22											
346	SCG - RFA Preparation	65 days	Sun 11/1/20	Thu 1/28/21											
347	SCG - RFA Release	1 day	Fri 2/19/21	Fri 2/19/21											
348	SCG - RFA Abstract Creation Duration	25 days	Mon 2/22/21	Fri 3/26/21											
349	SCG - RFA Evaluation	25 days	Mon 3/29/21	Fri 4/30/21											
350	SCG - RFA Review with EE PRG	0 days	Tue 5/4/21	Tue 5/4/21											
351	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/11/21	Tue 5/11/21											
352	SCG - RFP Preparation	42 days	Thu 4/1/21	Fri 5/28/21											
353	SCG - RFP Release	0 days	Fri 6/11/21	Fri 6/11/21											
354	SCG - RFP Proposal Creation Duration	30 days	Mon 6/14/21	Fri 7/23/21											
355	SCG - RFP Evaluation	30 days	Mon 7/26/21	Fri 9/3/21											
356	SCG - RFP Review with EE PRG	0 days	Tue 9/7/21	Tue 9/7/21											
357	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/14/21	Tue 9/14/21											
358	SCG - Contract Negotiation and Development	35 days	Mon 10/18/21	Fri 12/3/21											
359	SCG - Contract Review with EE PRG	9 days	Tue 12/7/21	Fri 12/17/21											
360	SCG - Final Award and Contract Signed	10 days	Mon 12/20/21	Fri 12/31/21											
361	SCG - Submit Advice Letter	21 days	Mon 1/3/22	Mon 1/31/22											
362	SCG - Advice Letter Approved	0 days	Fri 4/29/22	Fri 4/29/22											
363	SCG - Implementation Plan	44 days	Mon 5/2/22	Thu 6/30/22											
364	SCG - Public Sector Segment Solicitation	434 days	Sun 11/1/20	Thu 6/30/22											
365	SCG - RFA Preparation	65 days	Sun 11/1/20	Thu 1/28/21											
366	SCG - RFA Release	0 days	Fri 2/19/21	Fri 2/19/21											
367	SCG - RFA Abstract Creation Duration	25 days	Mon 2/22/21	Fri 3/26/21											
368	SCG - RFA Evaluation	25 days	Mon 3/29/21	Fri 4/30/21											
369	SCG - RFA Review with EE PRG	0 days	Tue 5/4/21	Tue 5/4/21											
370	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/11/21	Tue 5/11/21											
371	SCG - RFP Preparation	42 days	Thu 4/1/21	Fri 5/28/21											
372	SCG - RFP Release	0 days	Fri 6/11/21	Fri 6/11/21											
373	SCG - RFP Proposal Creation Duration	30 days	Mon 6/14/21	Fri 7/23/21											
374	SCG - RFP Evaluation	30 days	Mon 7/26/21	Fri 9/3/21											
375	SCG - RFP Review with EE PRG	0 days	Tue 9/7/21	Tue 9/7/21											
376	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/14/21	Tue 9/14/21											
377	SCG - Contract Negotiation and Development	35 days	Mon 10/18/21	Fri 12/3/21											
378	SCG - Contract Review with EE PRG	9 days	Tue 12/7/21	Fri 12/17/21											
379	SCG - Final Award and Contract Signed	10 days	Mon 12/20/21	Fri 12/31/21											
380	SCG - Submit Advice Letter	21 days	Mon 1/3/22	Mon 1/31/22											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1		
381	SCG - Advice Letter Approved	0 days	Fri 4/29/22	Fri 4/29/22											
382	SCG - Implementation Plan	44 days	Mon 5/2/22	Thu 6/30/22											
383	SCG - Local Industrial Solicitation	434 days	Tue 12/1/20	Sun 7/31/22											
384	SCG - RFA Preparation	63 days	Tue 12/1/20	Thu 2/25/21											
385	SCG - RFA Release	0 days	Fri 3/19/21	Fri 3/19/21											
386	SCG - RFA Abstract Creation Duration	25 days	Mon 3/22/21	Fri 4/23/21											
387	SCG - RFA Evaluation	25 days	Mon 4/26/21	Fri 5/28/21											
388	SCG - RFA Review with EE PRG	0 days	Tue 6/1/21	Tue 6/1/21											
389	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/8/21	Tue 6/8/21											
390	SCG - RFP Preparation	46 days	Sat 5/1/21	Fri 7/2/21											
391	SCG - RFP Release	0 days	Fri 7/16/21	Fri 7/16/21											
392	SCG - RFP Proposal Creation Duration	30 days	Mon 7/19/21	Fri 8/27/21											
393	SCG - RFP Evaluation	25 days	Mon 8/30/21	Fri 10/1/21											
394	SCG - RFP Review with EE PRG	0 days	Tue 10/5/21	Tue 10/5/21											
395	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 10/12/21	Tue 10/12/21											
396	SCG - Contract Negotiation and Development	46 days	Fri 10/29/21	Fri 12/31/21											
397	SCG - Contract Review with EE PRG	14 days	Tue 1/4/22	Fri 1/21/22											
398	SCG - Final Award and Contract Signed	6 days	Mon 1/24/22	Mon 1/31/22											
399	SCG - Submit Advice Letter	20 days	Tue 2/1/22	Mon 2/28/22											
400	SCG - Advice Letter Approved	0 days	Tue 5/31/22	Tue 5/31/22											
401	SCG - Implementation Plan	44 days	Wed 6/1/22	Sun 7/31/22											
402															
403	SDG&E - Small Commercial (<20kW)	656 days	Wed 8/1/18	Wed 2/3/21											
404	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18											
405	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18											
406	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18											
407	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19											
408	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19											
409	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19											
410	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19											
411	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19											
412	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19											
413	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19											
414	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20											
415	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20											
416	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20											
417	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20											
418	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
419	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20											
420	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20											
421	SDG&E - Implementation Plan	60 days	Thu 11/12/20	Wed 2/3/21											
422	SDG&E - Large Commercial (>20kW)	656 days	Wed 8/1/18	Wed 2/3/21	[Rollup Bar]										
423	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18											
424	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18											
425	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18											
426	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19											
427	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19											
428	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19											
429	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19											
430	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19											
431	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19											
432	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19											
433	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20											
434	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20											
435	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20											
436	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20											
437	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20											
438	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20											
439	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20											
440	SDG&E - Implementation Plan	60 days	Thu 11/12/20	Wed 2/3/21											
441	SDG&E - Residential Multi-Family	630 days	Thu 9/6/18	Wed 2/3/21	[Rollup Bar]										
442	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18											
443	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19											
444	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18											
445	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19											
446	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18											
447	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19											
448	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19											
449	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19											
450	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19											
451	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19											
452	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19											
453	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
454	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20											
455	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20											
456	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
457	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20											
458	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20											
459	SDG&E - Implementation Plan	60 days	Thu 11/12/20	Wed 2/3/21											
460	SDG&E - SW HVAC	586 days	Thu 11/1/18	Fri 1/29/21											
461	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19											
462	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19											
463	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19											
464	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19											
465	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19											
466	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19											
467	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19											
468	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19											
469	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19											
470	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19											
471	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
472	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
473	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20											
474	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20											
475	SDG&E - Final Award and Contract Signed	0 days	Wed 9/30/20	Wed 9/30/20											
476	SDG&E - Submit Advice Letter	0 days	Thu 11/19/20	Thu 11/19/20											
477	SDG&E - Advice Letter Approved														
478	SDG&E - Implementation Plan	0 days	Fri 1/29/21	Fri 1/29/21											
479	SDG&E - SW PLA	633 days?	Mon 1/28/19	Wed 6/30/21											
480	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19											
481	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19											
482	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19											
483	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19											
484	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19											
485	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19											
486	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19											
487	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20											
488	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20											
489	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20											
490	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20											
491	SDG&E - Selection Review with EE PRG	0 days	Tue 10/13/20	Tue 10/13/20											
492	SDG&E - Contract Negotiation and Development	51 days	Mon 11/2/20	Mon 1/11/21											
493	SDG&E - Contract Review with EE PRG	0 days	Tue 2/9/21	Tue 2/9/21											
494	SDG&E - Final Award and Contract Signed	0 days	Mon 2/22/21	Mon 2/22/21											

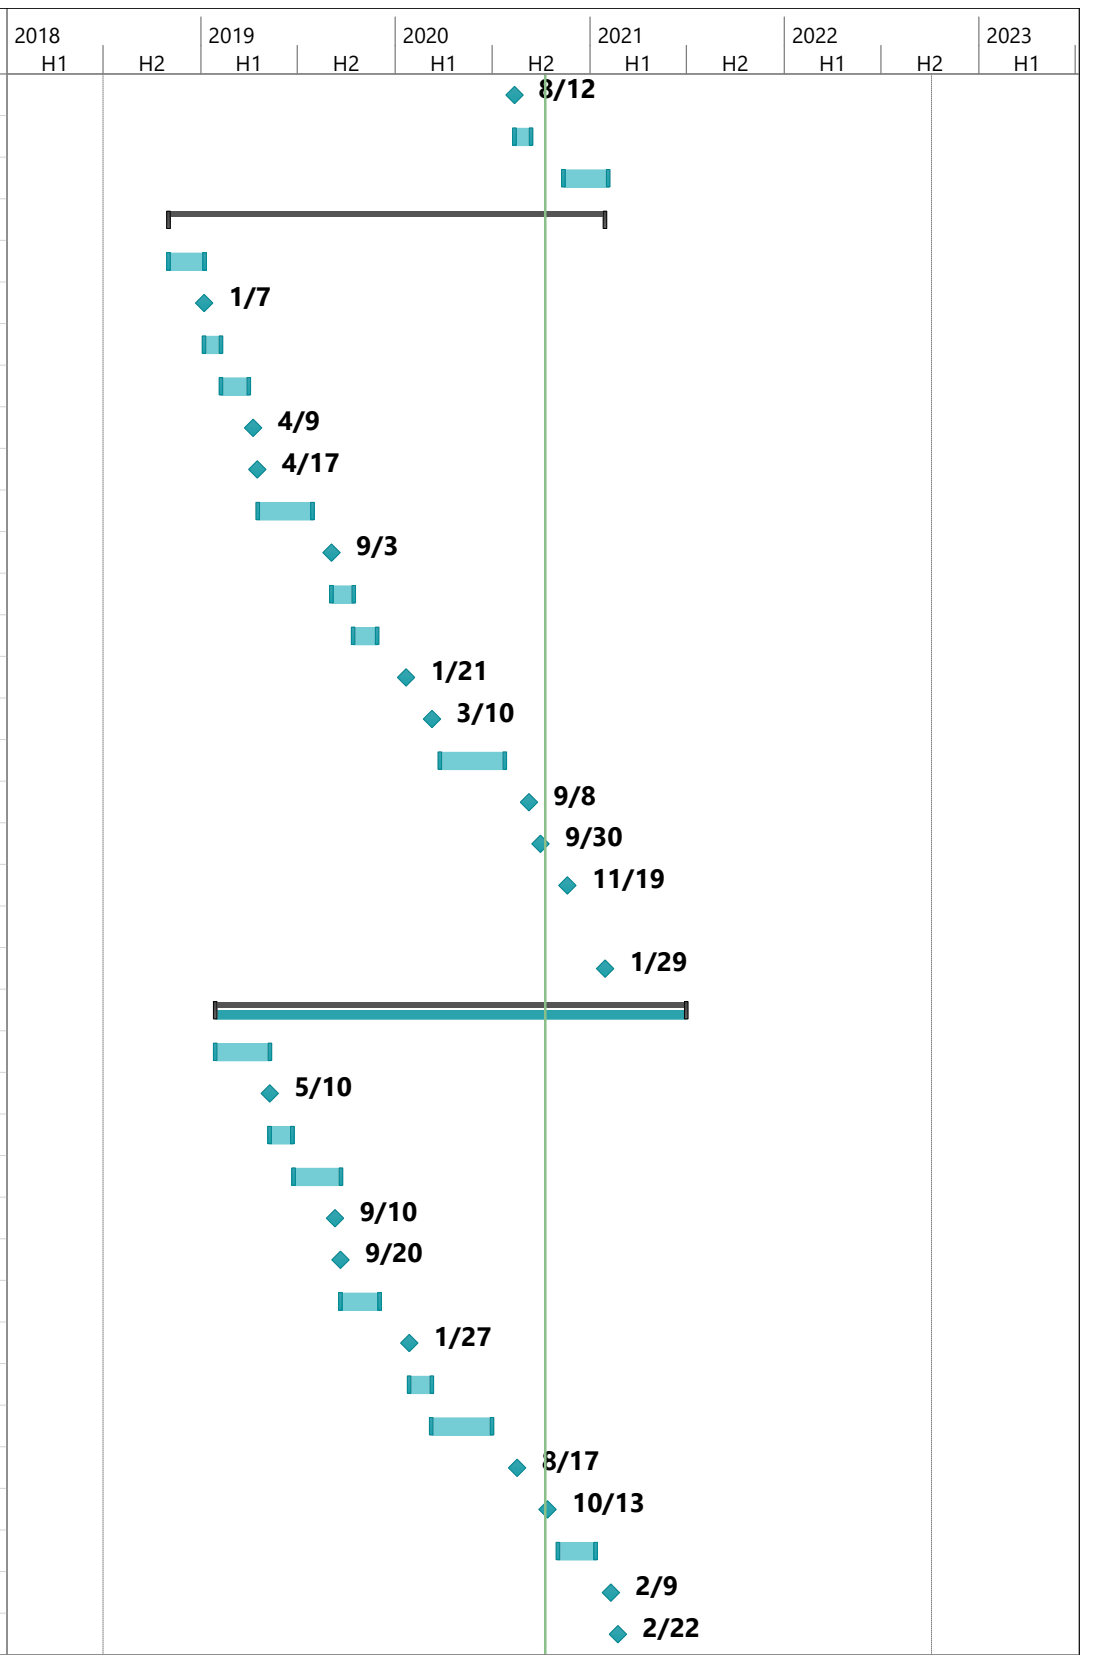

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
495	SDG&E - Submit Advice Letter	0 days	Tue 3/30/21	Tue 3/30/21											
496	SDG&E - Advice Letter Approved														
497	SDG&E - Implementation Plan	0 days	Wed 6/30/21	Wed 6/30/21											
498	SDG&E - Residential Single Family	457 days	Mon 7/1/19	Wed 3/31/21											
499	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19											
500	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19											
501	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19											
502	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20											
503	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19											
504	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20											
505	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20											
506	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20											
507	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20											
508	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20											
509	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20											
510	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20											
511	SDG&E - Contract Negotiation and Development	46 days	Mon 8/17/20	Mon 10/19/20											
512	SDG&E - Contract Review with EE PRG	10 days	Tue 11/10/20	Mon 11/23/20											
513	SDG&E - Final Award and Contract Signed	0 days	Mon 11/16/20	Mon 11/16/20											
514	SDG&E - Submit Advice Letter	0 days	Thu 12/31/20	Thu 12/31/20											
515	SDG&E - Advice Letter Approved														
516	SDG&E - Implementation Plan	0 days	Wed 3/31/21	Wed 3/31/21											
517	SDG&E - Federal	496 days	Mon 7/1/19	Tue 5/25/21											
518	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19											
519	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19											
520	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19											
521	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20											
522	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
523	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20											
524	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20											
525	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20											
526	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20											
527	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20											
528	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20											
529	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20											
530	SDG&E - Contract Negotiation and Development	45 days	Thu 11/19/20	Wed 1/20/21											
531	SDG&E - Contract Review with EE PRG	0 days	Tue 1/12/21	Tue 1/12/21											
532	SDG&E - Final Award and Contract Signed	0 days	Mon 1/25/21	Mon 1/25/21											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
533	SDG&E - Submit Advice Letter	0 days	Thu 2/25/21	Thu 2/25/21											
534	SDG&E - Advice Letter Approved														
535	SDG&E - Implementation Plan	0 days	Tue 5/25/21	Tue 5/25/21											
536	SDG&E - K-12	496 days	Mon 7/1/19	Tue 5/25/21											
537	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19											
538	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19											
539	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19											
540	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20											
541	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
542	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20											
543	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20											
544	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20											
545	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20											
546	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20											
547	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20											
548	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20											
549	SDG&E - Contract Negotiation and Development	45 days	Thu 11/19/20	Wed 1/20/21											
550	SDG&E - Contract Review with EE PRG	0 days	Tue 1/12/21	Tue 1/12/21											
551	SDG&E - Final Award and Contract Signed	0 days	Mon 1/25/21	Mon 1/25/21											
552	SDG&E - Submit Advice Letter	0 days	Thu 2/25/21	Thu 2/25/21											
553	SDG&E - Advice Letter Approved														
554	SDG&E - Implementation Plan	0 days	Tue 5/25/21	Tue 5/25/21											
555	SDG&E - Local Governments	304 days?	Tue 10/13/20	Fri 12/10/21											
556	SDG&E - RFA Preparation														
557	SDG&E - RFA Release														
558	SDG&E - RFA Abstract Creation Duration														
559	SDG&E - RFA Evaluation														
560	SDG&E - RFA Review with EE PRG														
561	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
562	SDG&E - RFP Preparation														
563	SDG&E - RFP Release														
564	SDG&E - RFP Proposal Creation Duration														
565	SDG&E - RFP Evaluation														
566	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
567	SDG&E - Selection Review with EE PRG														
568	SDG&E - Contract Negotiation and Development														
569	SDG&E - Contract Review with EE PRG														
570	SDG&E - Final Award and Contract Signed														

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1		
571	SDG&E - Submit Advice Letter														
572	SDG&E - Advice Letter Approved														
573	SDG&E - Implementation Plan														
574	*SDG&E - Agriculture Growers	304 days?	Mon 2/1/21	Thu 3/31/22											
575	SDG&E - RFA Preparation														
576	SDG&E - RFA Release														
577	SDG&E - RFA Abstract Creation Duration														
578	SDG&E - RFA Evaluation														
579	SDG&E - RFA Review with EE PRG														
580	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
581	SDG&E - RFP Preparation														
582	SDG&E - RFP Release														
583	SDG&E - RFP Proposal Creation Duration														
584	SDG&E - RFP Evaluation														
585	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
586	SDG&E - Selection Review with EE PRG														
587	SDG&E - Contract Negotiation and Development														
588	SDG&E - Contract Review with EE PRG														
589	SDG&E - Final Award and Contract Signed														
590	SDG&E - Submit Advice Letter														
591	SDG&E - Advice Letter Approved														
592	SDG&E - Implementation Plan														
593	*SDG&E - Industrial/Port Tenants	304 days?	Mon 2/1/21	Thu 3/31/22											
594	SDG&E - RFA Preparation														
595	SDG&E - RFA Release														
596	SDG&E - RFA Abstract Creation Duration														
597	SDG&E - RFA Evaluation														
598	SDG&E - RFA Review with EE PRG														
599	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
600	SDG&E - RFP Preparation														
601	SDG&E - RFP Release														
602	SDG&E - RFP Proposal Creation Duration														
603	SDG&E - RFP Evaluation														
604	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
605	SDG&E - Selection Review with EE PRG														
606	SDG&E - Contract Negotiation and Development														
607	SDG&E - Contract Review with EE PRG														
608	SDG&E - Final Award and Contract Signed														

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
609	SDG&E - Submit Advice Letter														
610	SDG&E - Advice Letter Approved														
611	SDG&E - Implementation Plan														
612	*SDG&E - SW Downstream Res HVAC	326 days?	Mon 7/5/21	Mon 10/3/22											
613	SDG&E - RFA Preparation														
614	SDG&E - RFA Release														
615	SDG&E - RFA Abstract Creation Duration														
616	SDG&E - RFA Evaluation														
617	SDG&E - RFA Review with EE PRG														
618	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
619	SDG&E - RFP Preparation														
620	SDG&E - RFP Release														
621	SDG&E - RFP Proposal Creation Duration														
622	SDG&E - RFP Evaluation														
623	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
624	SDG&E - Selection Review with EE PRG														
625	SDG&E - Contract Negotiation and Development														
626	SDG&E - Contract Review with EE PRG														
627	SDG&E - Final Award and Contract Signed														
628	SDG&E - Submit Advice Letter														
629	SDG&E - Advice Letter Approved														
630	SDG&E - Implementation Plan														
631	*SDG&E - Local/Residential Behavioral	324 days?	Mon 4/5/21	Thu 6/30/22											
632	SDG&E - RFA Preparation														
633	SDG&E - RFA Release														
634	SDG&E - RFA Abstract Creation Duration														
635	SDG&E - RFA Evaluation														
636	SDG&E - RFA Review with EE PRG														
637	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
638	SDG&E - RFP Preparation														
639	SDG&E - RFP Release														
640	SDG&E - RFP Proposal Creation Duration														
641	SDG&E - RFP Evaluation														
642	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
643	SDG&E - Selection Review with EE PRG														
644	SDG&E - Contract Negotiation and Development														
645	SDG&E - Contract Review with EE PRG														
646	SDG&E - Final Award and Contract Signed														

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
647	SDG&E - Submit Advice Letter														
648	SDG&E - Advice Letter Approved														
649	SDG&E - Implementation Plan														
650	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change														
651															
652	Local Multi-Sector (25% outsource)	572 days	Wed 8/1/18	Thu 10/8/20											
653	PG&E RFA Preparation	83 days	Wed 8/1/18	Fri 11/23/18											
654	PG&E RFA Release	1 day	Wed 11/28/18	Wed 11/28/18											
655	PG&E RFA Abstract Creation Duration	34 days	Wed 11/28/18	Mon 1/14/19											
656	PG&E RFA Evaluation	22 days	Fri 1/18/19	Mon 2/18/19											
657	PG&E RFA Review with EE PRG	3 days	Thu 2/21/19	Mon 2/25/19											
658	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/11/19	Fri 3/15/19											
659	PG&E RFP Preparation	75 days	Mon 2/25/19	Fri 6/7/19											
660	PG&E RFP Release	1 day	Wed 6/12/19	Wed 6/12/19											
661	PG&E RFP Proposal Creation Duration	37 days	Wed 6/12/19	Thu 8/1/19											
662	PG&E RFP Evaluation	120 days	Mon 8/5/19	Fri 1/17/20											
663	PG&E RFP Review with EE PRG	4 days	Tue 1/28/20	Fri 1/31/20											
664	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	11 days	Mon 2/3/20	Mon 2/17/20											
665	PG&E Contract Negotiation and Development	70 days	Mon 2/10/20	Fri 5/15/20											
666	PG&E Contract Review with EE PRG	6 days	Tue 5/26/20	Tue 6/2/20											
667	PG&E Final Award and Contract Signed	2 days	Tue 7/28/20	Wed 7/29/20											
668	PG&E Submit Advice Letter	9 days	Tue 6/30/20	Fri 7/10/20											
669	PG&E Advice Letter Approved														
670	PG&E Implementation Plan	23 days	Tue 9/8/20	Thu 10/8/20											
671	PG&E - Local Govt. Partner (non-resource programs)	376 days	Fri 3/22/19	Fri 8/28/20											
672	PG&E RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19											
673	PG&E RFA Release	0 days	Thu 5/23/19	Thu 5/23/19											
674	PG&E RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19											
675	PG&E RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19											
676	PG&E RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19											
677	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19											
678	PG&E RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19											
679	PG&E RFP Release	0 days	Mon 11/4/19	Mon 11/4/19											
680	PG&E RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19											
681	PG&E RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20											
682	PG&E RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20											
683	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	
684	PG&E Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20											
685	PG&E Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20											
686	PG&E Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20											
687	PG&E Submit Advice Letter		N/A	N/A											
688	PG&E Advice Letter Approved														
689	PG&E Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20											
690	PG&E - SW Codes & Standards (RFP only)	221 days	Mon 7/8/19	Mon 5/11/20											
691	PG&E RFA Preparation		N/A	N/A											
692	PG&E RFA Release		N/A	N/A											
693	PG&E RFA Abstract Creation Duration		N/A	N/A											
694	PG&E RFA Evaluation		N/A	N/A											
695	PG&E RFA Review with EE PRG		N/A	N/A											
696	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A											
697	PG&E RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19											
698	PG&E RFP Release	1 day	Tue 9/10/19	Tue 9/10/19											
699	PG&E RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19											
700	PG&E RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19											
701	PG&E RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19											
702	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19											
703	PG&E Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20											
704	PG&E Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20											
705	PG&E Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20											
706	PG&E Submit Advice Letter		N/A	N/A											
707	PG&E Advice Letter Approved														
708	PG&E Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20											
709	PG&E - Local Multi-Sector (40% outsource)	290 days	Tue 4/28/20	Mon 6/7/21											
710	PG&E RFA Preparation		N/A	N/A											
711	PG&E RFA Release		N/A	N/A											
712	PG&E RFA Abstract Creation Duration		N/A	N/A											
713	PG&E RFA Evaluation		N/A	N/A											
714	PG&E RFA Review with EE PRG		N/A	N/A											
715	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A											
716	PG&E RFP Preparation		N/A	N/A											
717	PG&E RFP Release		N/A	N/A											
718	PG&E RFP Proposal Creation Duration		N/A	N/A											
719	PG&E RFP Evaluation		N/A	N/A											
720	PG&E RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20											
721	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder														

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
722	PG&E Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20											
723	PG&E Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20											
724	PG&E Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20											
725	PG&E Submit Advice Letter	25 days	Mon 1/4/21	Fri 2/5/21											
726	PG&E Advice Letter Approved														
727	PG&E Implementation Plan	46 days	Mon 4/5/21	Mon 6/7/21											
728	PG&E - SW New Construction	576 days?	Mon 3/25/19	Mon 6/7/21											
729	PG&E RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19											
730	PG&E RFA Release	1 day	Tue 5/28/19	Tue 5/28/19											
731	PG&E RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19											
732	PG&E RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19											
733	PG&E RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19											
734	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19											
735	PG&E RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20											
736	PG&E RFP Release	1 day	Mon 3/16/20	Mon 3/16/20											
737	PG&E RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20											
738	PG&E RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20											
739	PG&E RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20											
740	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20											
741	PG&E Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20											
742	PG&E Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20											
743	PG&E Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20											
744	PG&E Submit Advice Letter	25 days	Mon 1/4/21	Fri 2/5/21											
745	PG&E Advice Letter Approved														
746	PG&E Implementation Plan	46 days	Mon 4/5/21	Mon 6/7/21											
747	SW WE&T K-12 Connections	357 days?	Tue 1/7/20	Wed 5/19/21											
748	PG&E RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20											
749	PG&E RFA Release	1 day	Mon 4/6/20	Mon 4/6/20											
750	PG&E RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20											
751	PG&E RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20											
752	PG&E RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20											
753	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20											
754	PG&E RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20											
755	PG&E RFP Release	1 day	Fri 9/4/20	Fri 9/4/20											
756	PG&E RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20											
757	PG&E RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20											
758	PG&E RFP Review with EE PRG	7 days	Tue 10/27/20	Wed 11/4/20											
759	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/5/20	Wed 11/11/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
760	PG&E Contract Negotiation and Development	24 days	Mon 11/16/20	Thu 12/17/20											
761	PG&E Contract Review with EE PRG	10 days	Mon 1/4/21	Fri 1/15/21											
762	PG&E Final Award and Contract Signed	66 days	Wed 11/18/20	Wed 2/17/21											
763	PG&E Submit Advice Letter	2 days	Fri 3/19/21	Mon 3/22/21											
764	PG&E Advice Letter Approved														
765	PG&E Implementation Plan	45 days	Tue 6/1/21	Mon 8/2/21											
766	SW WE&T Career and Workforce Readiness	410 days	Tue 1/7/20	Mon 8/2/21											
767	PG&E RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20											
768	PG&E RFA Release	1 day	Mon 4/6/20	Mon 4/6/20											
769	PG&E RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20											
770	PG&E RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20											
771	PG&E RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20											
772	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20											
773	PG&E RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20											
774	PG&E RFP Release	1 day	Fri 9/4/20	Fri 9/4/20											
775	PG&E RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20											
776	PG&E RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20											
777	PG&E RFP Review with EE PRG	7 days	Tue 10/27/20	Wed 11/4/20											
778	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/5/20	Wed 11/11/20											
779	PG&E Contract Negotiation and Development	61 days	Wed 11/18/20	Wed 2/10/21											
780	PG&E Contract Review with EE PRG	10 days	Thu 2/18/21	Wed 3/3/21											
781	PG&E Final Award and Contract Signed	41 days	Thu 3/4/21	Thu 4/29/21											
782	PG&E Submit Advice Letter	1 day	NA	NA											
783	PG&E Advice Letter Approved														
784	PG&E Implementation Plan	45 days	Tue 6/1/21	Mon 8/2/21											
785	SW State of California / Dept. of Corrections	348 days?	Sun 3/1/20	Tue 6/29/21											
786	PG&E RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20											
787	PG&E RFA Release	1 day	Wed 5/13/20	Wed 5/13/20											
788	PG&E RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20											
789	PG&E RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20											
790	PG&E RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20											
791	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20											
792	PG&E RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20											
793	PG&E RFP Release	1 day	Wed 9/9/20	Wed 9/9/20											
794	PG&E RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20											
795	PG&E RFP Evaluation	16 days	Fri 10/23/20	Fri 11/13/20											
796	PG&E RFP Review with EE PRG	6 days	Tue 11/24/20	Tue 12/1/20											
797	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 12/7/20	Fri 12/11/20											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
798	PG&E Contract Negotiation and Development	41 days	Fri 12/4/20	Fri 1/29/21											
799	PG&E Contract Review with EE PRG	5 days	Tue 2/23/21	Mon 3/1/21											
800	PG&E Final Award and Contract Signed	15 days	Mon 3/8/21	Fri 3/26/21											
801	PG&E Submit Advice Letter	1 day	Fri 4/30/21	Fri 4/30/21											
802	PG&E Advice Letter Approved														
803	PG&E Implementation Plan	44 days	Thu 5/20/21	Tue 7/20/21											

Project: IOU Master Task Timeli
Date: Fri 10/9/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
